

Project Manager · BBS operational course

Assigned projects, planning, operational review, corrections, reports and precise role handoffs

Actual role sessions · Exact controls · Saved outcomes · Recovery and handoffs

Project: BBS · Ejemplo de manual Number: C-0050-P-20261005

Read Before you practise before following any financial or operational training exercise. The training database is separate from the live portal.

Contents

Before you practise · access and scope	3
Start with your account and assigned scope	5
Find the right workspace on desktop and phone	8
Use Dashboard to decide where to act	11
Inspect the project before changing its team	13
Understand Team, assignments and review authority	15
Review submitted time and expenses operationally	19
Return a source and verify its linked replacement	22
Review Daily and Technical / PLC reports	25
Check period readiness and hand off customer sign-off	29
Publish a future plan without creating actual time	32
Change a published assignment and verify persistence	35
Follow a shared plan through crew work and review	37
Distinguish planned hours, expected hours and work goals	43
Maintain expertise and availability in the correct scope	53
Record your own operational time and hand it off	55
Inspect receipts and distinguish operational review from repayment	58
Read only your own compensation and payment status	60
Upload and retrieve private project evidence	62
Read notifications without confusing them with approvals	65
Manage your account and find the correct guide	67
Complete the PM operational cycle and hand off	70

Before you practise · access and scope

This English guide uses BBS · Ejemplo de manual, project C-0050-P-20261005. The screenshots were taken using the stated role in an isolated database running the application. Training entries, payments, approvals and documents are fictional. They do not prove a real bank transfer, accountant approval or customer acceptance.

The company portal at <https://j-aautomation.com/j-aautomation/app> is LIVE. Training uses a separate URL and database. Before practising, obtain the isolated URL, your own role account and permitted exercises from the company administrator; verify the BBS project number. Without isolated access, treat these screenshots as read-only demonstrations and perform only authorized real work.

Use your own credentials. Do not borrow an Owner, Finance or colleague account. A platform role, project assignment, review permission, supplier authorization and dated crew delegation are separate requirements. Changing one does not automatically grant the others.

Select English in the workspace language control to follow the labels used here. Some saved BBS record names remain in their original language. On a phone open the navigation drawer to see full workspace names. Recheck the selected project and date range after every navigation.

The eight Worker test accounts in the private credentials document use the same Worker workflow. Crew chief is a dated delegation attached to a Worker account. Supplier Coordinator and External Technician are restricted profiles attached to Worker accounts. This guide never includes account passwords.

Each screenshot is an exercise checkpoint. Later fictional role entries and financial events are additional to the original October 1–5 workbook totals. Reopening the project or selecting the same dates does not restore that checkpoint. Read captions before comparing amounts or states.

The assignment and expected-hours supplement uses a separate isolated October 20–23 synthetic exercise. Project access, a published work plan and a dated working-hours target are separate records. Workers record actual work and report progress independently; a plan never creates actual hours or a payment.

Verify the result

- Confirm your displayed account, role or supplier profile, the project number and the dates before saving.
- For training access, scope or reset help, contact the company administrator at admin@j-aautomation.com. Include the role, route, project number, time and visible error; omit passwords, cookies and private customer or worker documents.

Before you practise · access and scope · continued

If you get stuck

- An empty project selector often means missing or expired assignment or authorization. Ask the Owner to check coverage for the date you are entering; do not create a duplicate project.
- A form shown in a screenshot can depend on role, source state or effective date. Use the documented role handoff when a control is absent.

Start with your account and assigned scope

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: [Sign in](#) → [Dashboard](#)

The Project Manager coordinates assigned projects and reviews operational facts. Account access, project membership, review permission and crew delegation are separate records. Having the Project Manager role does not automatically assign every project or authorize financial decisions.

This guide uses the same saved BBS project as the Owner and other role guides. The fictional Project Manager account was created through Owner Team, signed in normally, assigned to BBS and granted Can review. The Owner configured the required dated internal-cost and compensation coverage. Those setup actions belong to the Owner; this guide never asks you to create a duplicate BBS project.

Do the task

1. Use your own invitation or company account. Open the portal sign-in screen, enter the account email and password, and choose Continue to workspace.
2. Check that the account shown in Profile is yours and the role is Project manager. Never use the Owner or another worker's credentials to reach a missing control.
3. Open Dashboard and confirm BBS is in your authorized project scope. Open Projects and identify C-0050-P-20261005 before recording or reviewing anything.
4. Ask the Owner to verify active account status, dated project membership and Can review before starting this exercise. Assignment and commercial coverage must include the work date; current access also depends on the current application date.

Verify the result

- Native login succeeded as the fictional Project Manager. Dashboard showed one authorized active project after the Owner completed dated membership.
- An assignment starting the following UTC day initially showed no current project. The Owner added genuine coverage for the current day through native controls; no role or session was fabricated.


If you get stuck

- If BBS is missing, stop recording and give the Owner the project reference, your account and intended work dates. Do not create a replacement project.

Start with your account and assigned scope · continued

- If a review control is missing, check membership dates and Can review separately from the role label.

Start with your account and assigned scope

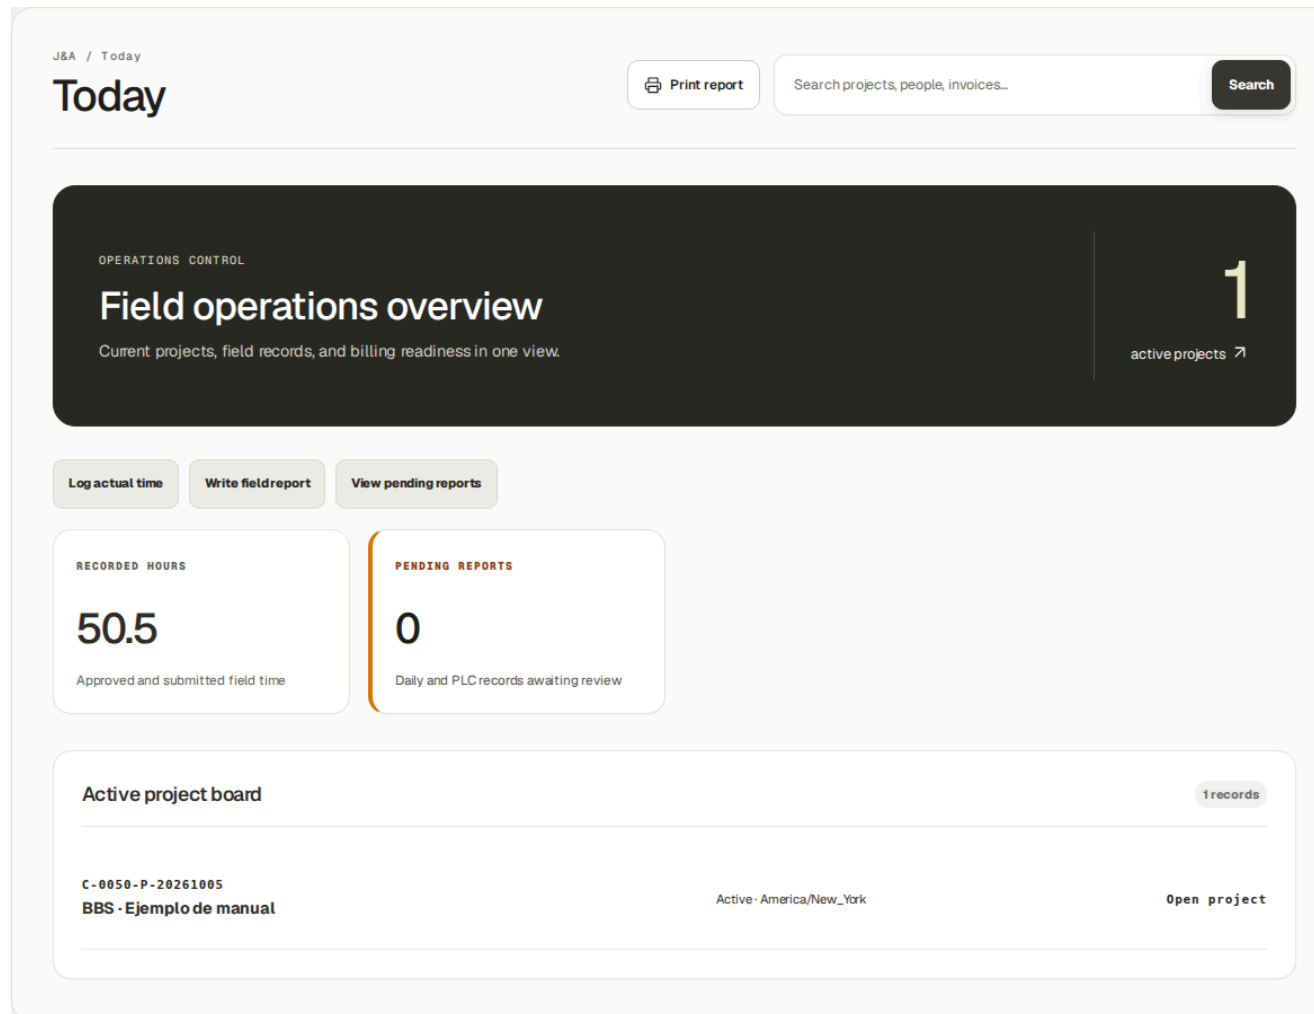

Actual Project Manager session: one authorized BBS project after native Owner onboarding.

Find the right workspace on desktop and phone

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Dashboard → primary navigation / More

Dashboard highlights operational activity. Projects holds project identity and scope; Approvals is the actionable review queue; Reports holds Daily, Technical / PLC and customer-follow-up views.

Time and Expenses are source registers. My Pay always concerns your own compensation. Team here is the operational directory and assignments, not Owner account administration. Planning publishes future assignments. Documents holds private project files; Profile holds expertise, availability and your security settings. Notifications and Help are separate destinations.

Do the task

1. On desktop select the named workspace in the sidebar. Keep the BBS project filter when changing registers.
2. On a phone use Dashboard, Projects, Approvals and Reports in the bottom navigation. Open More for the secondary workspaces.
3. Use the workspace filters rather than assuming every total concerns your own work. Time can show people across authorized projects; My Pay remains personal.
4. Use horizontal scrolling where the screen says Scroll horizontally to review all columns. Open a record to see its full facts before taking action.


Verify the result

- Actual PM navigation and Approvals were opened at 1440 desktop and 390 phone widths; the More drawer was captured.
- Planning was opened at 768 tablet width. These checks verify navigation and visible controls, not every device or browser.

If you get stuck

- If a drawer covers your content, close it or select a destination. Recheck the project and dates after navigation.
- Access restricted means the role cannot use that destination; return through Open my workspace and ask the Owner about the business handoff.

Find the right workspace on desktop and phone

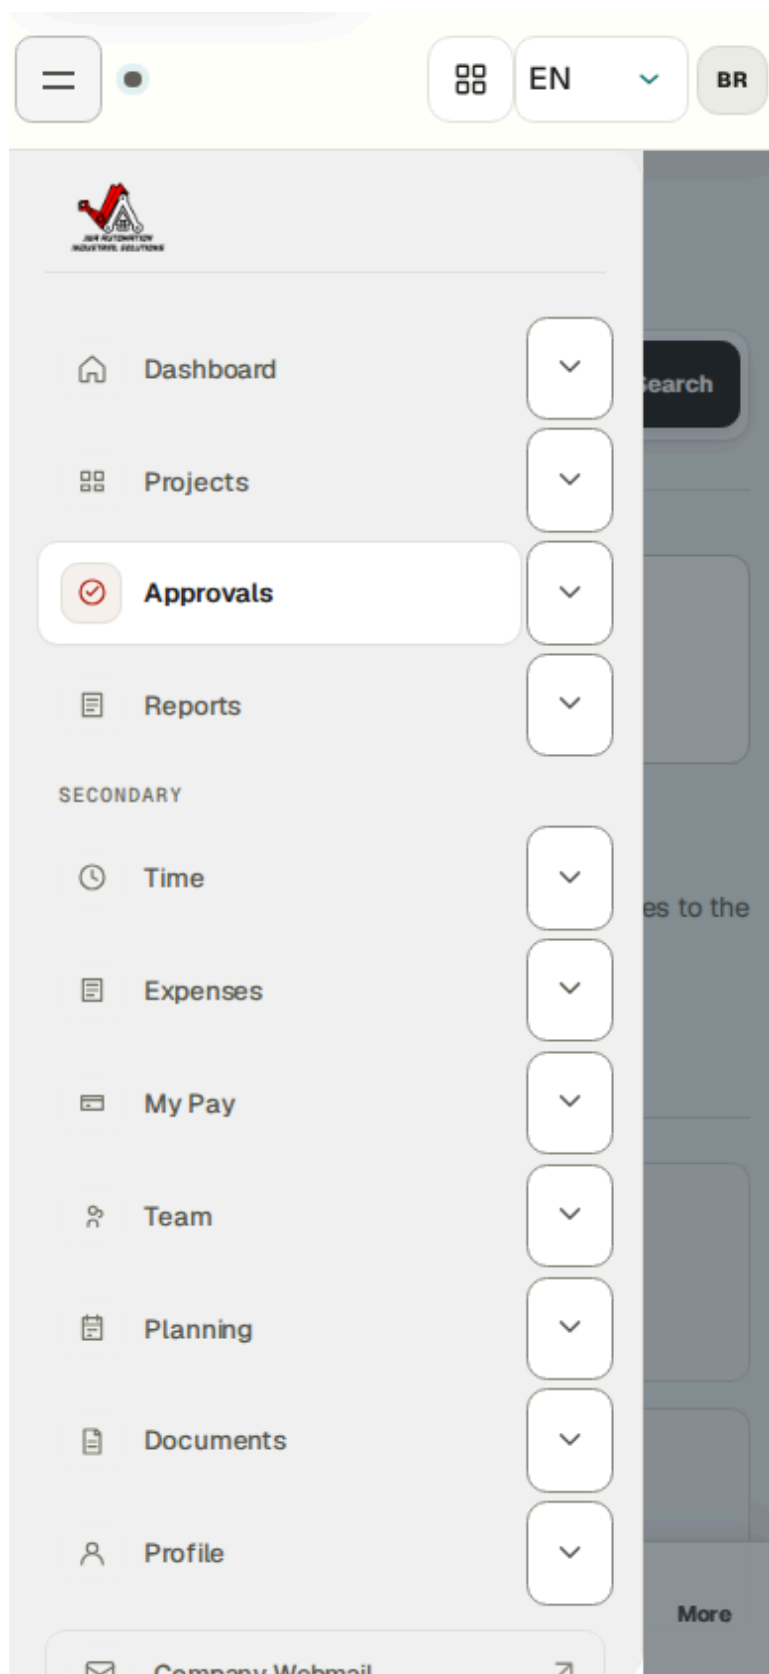

Actual PM phone session: More exposes secondary workspaces.

Find the right workspace on desktop and phone

≡

● Online

☰

🔔

✉ Webmail

EN ▼

BR

BBS ROLE LAB Project ...
Manager ▼

J&A / Resource planning

Resource planning

🖨 Print report

Search projects, people, invoices...

Search

Archived projects are hidden.

Include archived projects

October 2026

< Today >

Select a day to see its agenda. Times shown in UTC.

Mon	Tue	Wed	Thu	Fri	Sat	Sun
28 .	29 .	30 .	1 .	2 .	3 .	4 .
5 .	6 .	7 .	8 .	9 .	10 .	11 .
12 .	13 .	14 .	15 .	16 1	17 .	18 .
19 .	20 .	21 .	22 .	23 .	24 .	25 .
26 .	27 .	28 .	29 .	30 .	31 .	1 .
2 .	3 .	4 .	5 .	6 .	7 .	8 .

Monday, October 5, 2026

No events on this day.

Calendar times are shown in UTC. Planning never creates actual hours.

Published assignments

BBS DEMO - Tecnico 2 · C-0050-P-20261005 · 2026-10-16 08:00 → 2026-10-16 10:00

▼

Actual PM tablet session: BBS planning calendar.

Use Dashboard to decide where to act

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Dashboard → authorized project

Dashboard provides operational oversight. Recorded hours and activity counts are not invoice revenue, compensation settlements or cash collected. Open the underlying register to inspect its scope and state.

Do the task

1. Open Dashboard and identify the BBS project card and visible operational totals.
2. Choose the project or workspace behind an attention item. In Approvals use the BBS project and the work-date range to isolate the pending source.
3. Inspect the record and its history before deciding whether the facts are complete. Review daily work, expenses and reports in their own queues.


Verify the result

- The fictional PM dashboard displayed only authorized BBS project oversight. Financial portfolio workspaces were absent.
- A cleared queue is a completion check; it does not replace inspecting an actionable record first.

If you get stuck

- If the number differs from a register, compare date range, workers, state filters and whether the dashboard figure means recorded or reviewed activity.
- Escalate economic or billing questions to Finance or the Owner rather than interpreting operational hours as money.

Use Dashboard to decide where to act

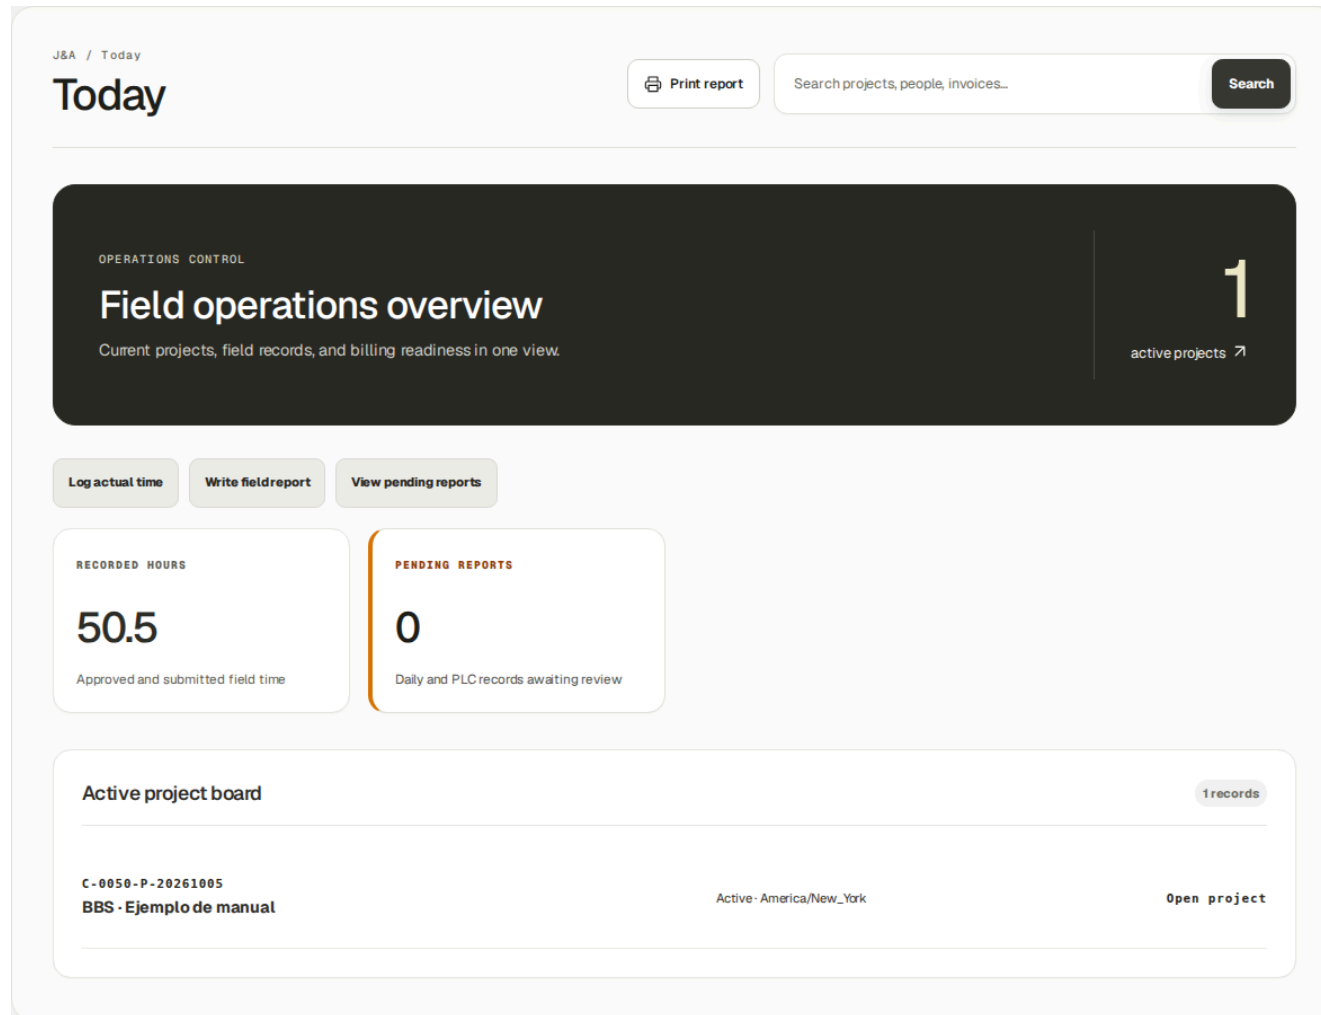

Actual PM Dashboard: operational oversight of the BBS training project.

Inspect the project before changing its team

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Projects → BBS → Overview

Project identity includes reference, client, status, schedule and timezone. BBS uses America/New_York for source work context, while Planning explicitly uses UTC. Your project Overview, Team and Reports / files views expose operational information.

Do the task

1. Open Projects. Use Search projects or Status, then Apply filters to find C-0050-P-20261005.
2. Open BBS and confirm the client, active status, planned start and timezone in Overview.
3. Open Team to inspect who is assigned and use Reports / files to reach project outputs and evidence.
4. Before making an assignment change, compare the intended work dates with existing coverage and the worker's availability.

Verify the result

- Native PM project detail and Team were opened. The project was scoped to BBS.
- The three canonical BBS invoice records were preserved; this PM packet created no project duplicate or invoice.

If you get stuck

- Include archived projects only when looking for historical work. Do not reopen or duplicate archived work to circumvent a blocked source.
- Project closing, commercial contracts and company billing belong to the authorized Owner/Finance process. Seek that handoff when those controls are unavailable.

Inspect the project before changing its team

The screenshot displays the BBS Project Manager interface. On the left is a sidebar with navigation options: Dashboard, Projects (selected), Approvals, Reports, SECONDARY, Time, Expenses, My Pay, Team, Planning, Documents, Profile, and a Company Webmail link. The main content area shows the project details for 'C-0050 - C-0050-P-20261005', which is 'Active'. The project title is 'BBS · Ejemplo de manual' with a subtitle 'BBS DEMO - Manual'. Three summary cards are shown: 'ACTUAL TIME' at 59.50h, 'ASSIGNED TEAM' of 7, and 'REPORTS' of 7. Below these are tabs for 'Overview' (selected), 'Team', and 'Reports & Files'. The 'Overview' tab contains a 'PROJECT CONTEXT' section with details like Client (BBS DEMO - Manual), Project Number (C-0050-P-20261005), and a table of operational expenses. The 'OPERATIONS' section shows a list of expenses, including 'BBS LAB fictional external tools' for USD 8.00 and 'BBS LAB fictional crew meal' for USD 20.00.

Online Go to section #/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

← Back

← Projects / C-0050-P-20261005

Print report Operations dashboard

C-0050 · C-0050-P-20261005 Active

BBS · Ejemplo de manual

BBS DEMO - Manual · — · —

ACTUAL TIME 59.50h Recorded operational time

ASSIGNED TEAM 7 Current project assignment(s)

REPORTS 7 Daily and technical records

Overview Team Reports & Files

PROJECT CONTEXT Overview Active

CLIENT	CLIENT NUMBER
BBS DEMO - Manual	C-0050
PROJECT NUMBER	COST CENTER
C-0050-P-20261005	BBS-DEMO-20261005
PO / REFERENCE	SITE / PLANT
Not configured	Not configured
TIMEZONE	SCHEDULE
America/New_York	2026-10-01 → —

PROYECTO DE DEMOSTRACION. Equipo, horas y gastos ficticios para el manual. No facturar ni pagar realmente.

OPERATIONS Operational expenses 7

Reported operational amounts and approval state. No commercial treatment is inferred.

Filter by category

All categories

E	BBS LAB fictional external tools	USD 8.00
2026-10-07 · Tools / consumables · Approved		
E	BBS LAB fictional crew meal	USD 20.00
2026-10-06 · Meals · Approved		

Actual PM project Overview: authorized BBS operational scope.

Understand Team, assignments and review authority

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Team → Project assignments

Team shows specialists in operational scope, availability, assignments and activity. An account can be Active yet lack dated project access. An assignment can exist without review permission. Chief delegation is another dated authorization and does not grant operational approval.

The PM browser exposed Assign worker, Update assignment and Remove assignment controls with dates. Owner-only commercial and review-permission fields were not shown in those PM forms. Existing historical assignments were inspected and left unchanged.

Do the task

1. Open Team and search the person by name or email. Confirm that this is the existing person record, avoiding a duplicate.
2. Open the Project assignments count. Identify the BBS assignment and inspect Starts on and Ends on.
3. For a genuinely authorized new assignment, open Assign worker, select BBS and the existing worker, enter dates, and choose Assign. This assignment mutation is a reference procedure here; this packet did not change another worker's historical membership.
4. For a date change use Update assignment on the correct person/project, then re-open and verify persistence. If removing access is required, use Remove assignment with a reason and coordinate the effects on future work.
5. Ask the Owner for Can review or chief delegation changes; do not assume changing project dates grants these permissions.

Verify the result

- Native PM Team listed BBS people and the actual assignment controls. The guide distinguishes inspected controls from executed assignment changes.
- All shared account/assignment/supplier bootstrap in this exercise was performed by the Owner through native forms.

Understand Team, assignments and review authority · continued

If you get stuck

- If Assign returns a coverage or state error, preserve the record and send the Owner the dates and intended person. Required commercial coverage is an Owner prerequisite.
- If a supplier technician lacks login access, an operational directory record is not enough: the Owner must create/link the permitted access profile.

Understand Team, assignments and review authority

The screenshot displays the J&A Team access interface. On the left is a sidebar with navigation links: Dashboard, Projects, Approvals, Reports, SECONDARY, Time, Expenses, My Pay, Team (highlighted), Planning, Documents, Profile, Company Webmail, and Sign out. The top navigation bar includes 'Online', 'Go to section', a search bar, and user information for 'BBS ROLE LAB Project Manager'. The main content area is titled 'Team access' and includes a 'Print report' button and a search bar. Below this, there's a section for 'Archived projects are hidden' with an 'Include archived projects' button. The 'OPERATIONAL DIRECTORY' section shows 'Team' with 6 members and a description: 'Active specialists, availability and project assignments.' A search bar for the team is present, along with filters for 'Search', 'Status' (set to 'All'), and 'Sort by' (set to 'Needs attention first'). The team list shows 1-6 / 6 members. The first member is 'BBS DEMO - Jefe de crew', a Worker with ID 'BD' and email 'bbs-manual-chief-20261005@example.test', who is 'Active'. Below the member name are four summary boxes: 'AVAILABILITY' (Active), 'ASSIGNMENTS' (1), 'PLANNED HOURS' (—), and 'ACTUAL HOURS' (12.25h). A 'Project assignments' button is at the bottom.

Dashboard

Projects

Approvals

Reports

SECONDARY

Time

Expenses

My Pay

Team

Planning

Documents

Profile

Company Webmail

Sign out

Online

Go to section

Webmail

EN

BR

BBS ROLE LAB Project Manager

J&A / Team access

Print report

Search projects, people, invoices...

Search

Archived projects are hidden.

Include archived projects

OPERATIONAL DIRECTORY

Team

Active specialists, availability and project assignments.

Search team

Name, role or project

Include inactive specialists

Search

Status

Sort by

All

Needs attention first

1-6 / 6

BBS DEMO - Jefe de crew

Worker

BD

bbs-manual-chief-20261005@example.test

Active

AVAILABILITY

Active

ASSIGNMENTS

1

PLANNED HOURS

—

ACTUAL HOURS

12.25h

Project assignments

Actual PM Team: existing BBS people and operational assignment summaries.

Understand Team, assignments and review authority

The screenshot displays the 'Team access' page in the J&A system. The left sidebar contains navigation links: Dashboard, Projects, Approvals, Reports, SECONDARY (Time, Expenses, My Pay, Team, Planning, Documents, Profile), and Company Webmail. The main content area is titled 'Team access' and includes a search bar and a 'Print report' button. Below this, a message states 'Archived projects are hidden.' with an 'Include archived projects' button. The 'PROJECT WORKSPACE' section is titled 'Projects' and provides a description: 'Review project identity, status, schedule and operational scope.' It features three summary cards: 'Active' (1 Operational projects), 'Planned' (0 Preparing to start), and 'Needs attention' (0 Paused or closing). A search section allows filtering by 'Project, client or reference' and 'Status' (Active), with 'Apply filters' and 'Clear filters' buttons. At the bottom, there is a 'Project calendar' dropdown and an 'Authorized projects' section with a 'Sort by' option.

Online Go to section: %/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

J&A / Team access

Print report Search projects, people, invoices... Search

Archived projects are hidden. Include archived projects

PROJECT WORKSPACE

Projects

Review project identity, status, schedule and operational scope.

Active 1 Operational projects

Planned 0 Preparing to start

Needs attention 0 Paused or closing

Search projects Status

Project, client or reference Active

Apply filters Clear filters

Project calendar

Authorized projects

Sort by

Actual PM assignment forms: operational date controls, without Owner financial setup.

Review submitted time and expenses operationally

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Approvals → Time / Expenses

Operational approval confirms the work or expense facts. Finance review later determines customer billing and expense treatment. Approving does not invoice the client, settle pay or reimburse a worker.

The queue remembers its selected tab. Always check Time, Expenses or Reports visibly; a saved Expenses tab can hide the time item you expected.

Do the task

1. Open Approvals. Select BBS, enter From and To, select the intended tab and choose Apply filters.
2. Use Needs attention or Status Submitted. Open the source record to inspect date, person, actual duration or receipt, activity and any correction history.
3. For correct time or expense facts, choose Approve on that source's card. Confirm the resulting state is Approved and it moves to completed follow-up/Finance review.
4. For incorrect facts, open Review actions, enter the Required change reason, and choose Needs changes. State exactly what the author should correct.
5. Use Reject only for a justified rejection with the required reason. This rejection path was not executed in the training packet.

Verify the result

- Genuine PM approval succeeded for submitted worker/chief time, Daily and Technical reports, the synthetic USD 12 worker expense, USD 20 shared meal and USD 8 external expense.
- PM review did not change customer billability, reimbursement entitlement, invoice state or recorded payments.

If you get stuck

- If a source is missing, check the tab, dates, project, worker and status. Refresh after new account/assignment creation and open the exact source from its author's handoff.
- If the permitted review still does not appear, send its ID and scope to the Owner. The coordinator's own Oct 8 time was not displayed in this PM queue; it remains submitted for an authorized handoff.

Review submitted time and expenses operationally

BBS DEMO - Tecnico 1 - 2026-10-06

Tools / consumables · BBS LAB fictional supplies

Operational review · BBS · Ejemplo de manual

● Submitted

Open record →

Before you continue

Approving confirms the time or expense facts and moves this record to Finance review. It does not decide customer billing or worker reimbursement.

[Review this record](#)


Approve

Review actions



Actual PM actionable expense review: operational approval is distinct from Finance treatment.

Review submitted time and expenses operationally

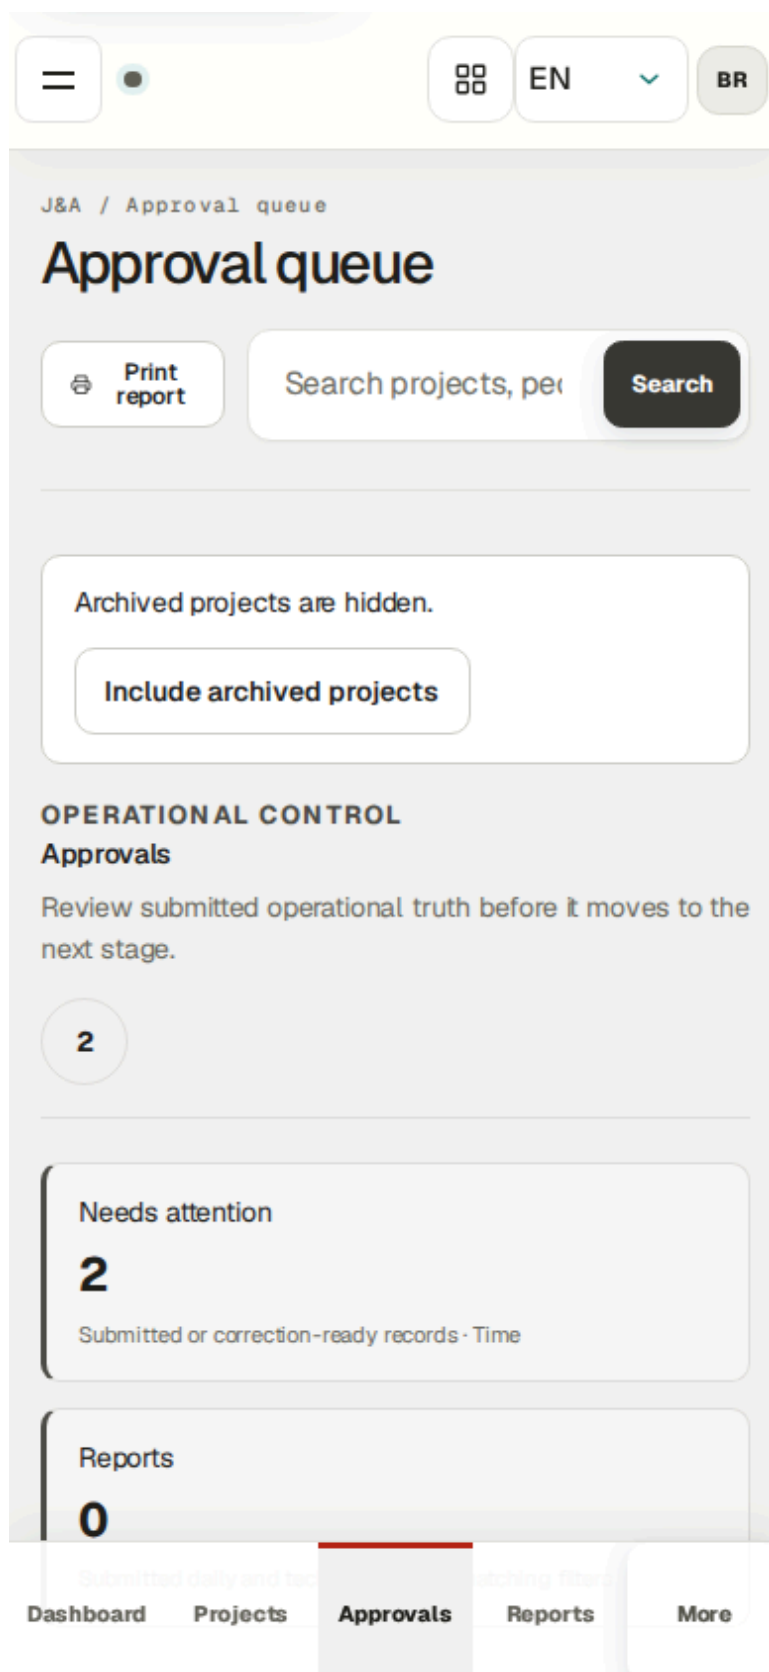

Actual PM Approvals on a phone: verify filters and tab before reviewing.

Return a source and verify its linked replacement

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Approvals → Time → Review actions

Submitted or returned sources are not silently edited in place. The author creates a linked correction draft with changed operational facts and a reason, explicitly submits it, and the PM reviews the replacement. The original remains in history.

The positive exercise used Worker 2 on October 15, outside that worker's finalized October 1–14 settlement. A Worker 1 October 6 correction was correctly blocked by the worker's finalized October 1–31 settlement; an audited Finance adjustment is a separate handoff.

Do the task

1. Find Worker 2's submitted October 15 3-hour source. Open Review actions, enter that actual training work was 2.5 hours, and choose Needs changes.
2. Give the source and reason to the worker. The worker uses Create corrected draft and Submit through their own account.
3. Find the submitted 2.5-hour replacement, open its correction reason and original link, then choose Approve if the changed facts are correct.
4. Repeat for the chief-recorded Worker 2 1-hour source: return it for 0.75 hour; the chief creates and submits the linked correction in the delegated workflow.
5. Approve the submitted 0.75-hour replacement. Verify the author's current October 15 activity is 3.25 hours: 2.5 own +0.75 delegated. The original 3+1 hours must not both count again.

Verify the result

- Both genuine PM replacements were Approved: 150 and 45 minutes. Both originals remained Needs changes.
- Worker and Chief guide captures verify the current 3.25-hour total. No finalized settlement or original invoice was modified.

If you get stuck

- If correction creation is blocked by finalized coverage or billing, stop and refer the exact source and error to Finance/Owner. Do not add an unrelated new time entry as a substitute.

Return a source and verify its linked replacement · continued

- If the correction has not been submitted, tell its author to use the linked detail's Submit. A draft alone is not ready for operational approval.

Return a source and verify its linked replacement

BBS DEMO - Tecnico 2 - 2026-10-15

Operational review · BBS · Ejemplo de manual

Open record →

Submitted

Before you continue

Approving confirms the time or expense facts and moves this record to Finance review. It does not decide customer billing or worker reimbursement.

[Review this record](#)

Approve

Review actions

Required change

ROLE GUIDE: actual training work was 2.5 hours, correct and resubmit

Before you continue

Returning asks the worker to correct the record's factual details. State the specific change needed; this does not decide customer billing or reimbursement.

[Review this record](#)

Needs changes

Rejection reason

Reject

Actual PM return: a specific Required change reason begins the correction handoff.

Review Daily and Technical / PLC reports

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Reports → Daily / Technical / PLC → Approvals Reports

Daily reports capture shift summary, completed tasks, problems, corrective action and next-day plan. Technical / PLC reports capture technical changes and rationale. These narratives complement actual hours; neither creates time or proves customer acceptance.

A worker or chief submits the report. The PM reviews assigned-project operational facts; Finance or Owner subsequently creates customer period outputs and records genuine signed evidence.

Do the task

1. Open Reports, filter BBS and the work dates, and select Daily or Technical / PLC.
2. Open the submitted report. Check who performed work, who created it, its version, date, narrative and private attachments.
3. Open Approvals and select Reports. Choose Approve report for a complete source, or return it with a specific reason through the available review action.
4. Reopen Reports and verify Approved and Reviewed by your PM account. Approved report content can then contribute to authorized customer-safe period output.
5. For your own operational reporting, New daily report or New technical report opens the source form. Save the draft and explicitly Submit for review; another authorized reviewer performs your review. Own PM report creation was not executed in this packet.

Verify the result

- PM Approved worker, chief, external technician and coordinator Daily reports, plus worker/chief/external Technical reports, using their real submitted source IDs.
- The report register displayed the actual PM reviewer attribution. No real equipment change or live dispatch is asserted by these synthetic narratives.

If you get stuck

- Return incomplete narratives rather than approving a blank or ambiguous report. The author must change the supported draft/correction and resubmit.

Review Daily and Technical / PLC reports · continued

- If a preview or attachment fails, inspect the preserved source fields, report the exact failure, and avoid treating a missing preview as customer acceptance. The restricted supplier own-report preview defect found during testing was fixed; their own object is permitted and another worker's remains denied.

Review Daily and Technical / PLC reports

The screenshot displays the 'Daily and technical reports' section of the J&A Automation BBS Role Manual interface. The interface is divided into a left sidebar and a main content area.

Left Sidebar:

- Dashboard
- Projects
- Approvals
- Reports** (highlighted)
- SECONDARY
 - Time
 - Expenses
 - My Pay
 - Team
 - Planning
 - Documents
 - Profile
- Company Webmail
- Sign out

Main Content Area:

- Top navigation: Online, Go to section, Webmail, EN, BR, BBS ROLE LAB Project Manager.
- Section title: **Daily and technical reports** (with a 'Print report' button).
- Search bar: Search projects, people, invoices... (with a 'Search' button).
- Archived projects: Archived projects are hidden. (with an 'Include archived projects' button).
- Period review and customer follow-up.
- OPERATIONS / REPORTS** (with a '6' badge): Reports. Capture field activity, technical changes and customer confirmation in one register.
- Project review workflow**: Review the operational facts for assigned projects and return incomplete records for correction. Customer reports contain approved work details without money. Other workers' compensation stays restricted; your own compensation is available separately in My Pay.
- New daily report** (red button) and **New technical report** (grey button).
- Needs attention**: 0. Draft, submitted, or returned field reports.
- Ready for signature**: 0. Customer confirmations awaiting signature.
- Customer sign-off**: 0. Period confirmations in scope.
- Search register**: Project, worker or report.
- Project**: C-0050-P-20261005 — BBS · Ejemplo de manual.
- Status**: All statuses.

Actual PM report register: approved fictional BBS narratives with reviewer attribution.

Review Daily and Technical / PLC reports

BBS DEMO - Jefe de crew - 2026-10-06

Technical report · BBS ROLE GUIDE - chief fictional bench

Report review · BBS · Ejemplo de manual

● Submitted

Open record →

Approve report

Review actions



Actual PM technical-report approval result for the chief's synthetic source.

Check period readiness and hand off customer sign-off

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Reports → Period review and customer follow-up / Client Sign-off

Customer acceptance applies to an exact report version and signed evidence, not an entire date range or all project work. A replacement report is required when a signed report's underlying content changes.

The PM interface explicitly assigns customer-safe period file generation to Finance/Owner and recording the customer's signed copy to an authorized Owner/Finance user. Operational review is your handoff.

Do the task

1. Open Reports and choose Period review and customer follow-up.
2. Select BBS, enter Period start and Period end, and choose Review period.
3. Inspect the Customer report queue for version, period and readiness. Use Client Sign-off to locate Needs report, Ready for signature, Signed or Invalid / superseded records in the same project/date scope.
4. If no customer report covers the period, send Finance/Owner the approved sources and intended dates. Do not mark operational approval as customer consent.
5. After Finance/Owner prepares a report, compare its exact version with the genuine signed evidence and ask the authorized user to complete the evidence-bound sign-off workflow.

Verify the result

- Native PM Review period for BBS October 6–31 showed no customer report; no acceptance was invented.
- Customer-follow-up and sign-off screens were opened as PM and displayed the explicit Owner/Finance handoff without financial amounts.

If you get stuck

- If a report was superseded or its sign-off invalidated, use the replacement version and obtain the required genuine evidence. Preserve the old record and PDF.
- PM customer sign-off mutation was not executed and is not claimed as a permitted shortcut.

Check period readiness and hand off customer sign-off

The screenshot displays the BBS ROLE LAB Project Manager interface. On the left is a sidebar with navigation options: Dashboard, Projects, Approvals, Reports (highlighted), and a 'SECONDARY' section with Time, Expenses, My Pay, Team, Planning, Documents, and Profile. At the bottom of the sidebar is a 'Sign out' button. The top header includes a status bar with 'Online', a 'Go to section' dropdown, a notification bell, a 'Webmail' button, a language dropdown set to 'EN', and a user profile for 'BBS ROLE LAB Project Manager' with a 'Manager' role. The main content area has a 'Back' button and a 'Back to Reports' link. The title 'Period review and customer follow-up' is prominently displayed, with a subtitle explaining the purpose: 'Review customer report versions, source coverage, billing readiness and private operational follow-up for one project period.' A 'Language' dropdown is set to 'English'. Below this is a 'Project period' section with three input fields: 'Project' (set to 'C-0050-P-20261005 — BBS · Ejemplo de'), 'Period start' (set to '10/06/2026'), and 'Period end' (set to '10/31/2026'). Each field has a 'Required' label and a calendar icon. A 'Review period' button is located below these fields. The next section, 'PROJECT PERIOD 2026-10-06 → 2026-10-31', includes a note: 'Acceptance is derived per exact customer report and its signed evidence. This period is not accepted as a whole.' Below this is a 'Customer report queue' section stating 'No customer reports cover this project period.' The final section, 'Finance billing readiness', states 'No finance amounts or billing details are shown here.'

Actual PM period review: no exact customer report covers this synthetic period.

Check period readiness and hand off customer sign-off

The screenshot displays the J&A Automation BBS Role Manual interface. The left sidebar contains navigation links: Dashboard, Projects, Approvals, Reports (highlighted), SECONDARY, Time, Expenses, My Pay, Team, Planning, Documents, Profile, Company Webmail, and Sign out. The main content area is titled 'Daily and technical reports' and includes a 'Print report' button and a search bar. Below the title, there is a section for 'Archived projects are hidden' with an 'Include archived projects' button. A 'Period review and customer follow-up' section is also present. The 'OPERATIONS / REPORTS' section shows 'Reports' with a description: 'Capture field activity, technical changes and customer confirmation in one register.' A 'Project review workflow' section provides instructions on reviewing operational facts and returning incomplete records. At the bottom, there are three status boxes: 'Needs attention' (0), 'Ready for signature' (0), and 'Customer sign-off' (0). A 'Filter reports' button is located at the bottom right.

Online Go to section: #/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

J&A / Daily and technical reports

Print report Search projects, people, invoices... Search

Archived projects are hidden. Include archived projects

Period review and customer follow-up

OPERATIONS / REPORTS Reports 6

Capture field activity, technical changes and customer confirmation in one register.

Project review workflow

Review the operational facts for assigned projects and return incomplete records for correction.

Customer reports contain approved work details without money. Other workers' compensation stays restricted; your own compensation is available separately in My Pay.

New daily report New technical report

Needs attention
0
Draft, submitted, or returned field reports

Ready for signature
0
Customer confirmations awaiting signature

Customer sign-off
0
Period confirmations in scope

Filter reports

Actual PM Client Sign-off: role handoff explains who generates and records acceptance.

Publish a future plan without creating actual time

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Planning → Publish field assignment

Planning is an expectation and coordination tool. It does not create recorded work, approvals, invoice units or worker pay. Planning and worker agendas explicitly display UTC.

The positive BBS exercise published a future October 16 08:00–10:00 UTC assignment for Worker 2, planned 2 hours, fictional bench site and required expertise.

Do the task

1. Open Planning and select BBS in Publish field assignment.
2. Select the existing assigned worker(s). Verify availability and assignment coverage for the intended date.
3. Enter Start (UTC), optional End (UTC), optional Planned hours, Site and Required expertise. Use the actual agreed schedule; do not convert site-local time silently.
4. Choose Publish assignment. Open the October 16 day and the Published schedule record.
5. Confirm the selected worker, UTC start/end and 120 planned minutes. Ask the worker to verify their agenda; they still record actual work independently afterward.

Verify the result

- Native PM Publish assignment succeeded. Worker 2's separate role session saw the published plan.
- A read-only database check found zero BBS actual time entries on October 16 after publication and update.

If you get stuck

- If the worker is absent, verify dated project assignment and availability with Owner/Team. Publishing is not a substitute for project membership.
- If dates are wrong, use the published record's update workflow rather than creating an overlapping duplicate plan.

Publish a future plan without creating actual time

Online

Go to section ⌘/Ctrl K

Webmail

EN

BR BBS ROLE LAB Project Manager Manager

worker records the work performed separately.

Project

C-0050-P-20261005 — BBS · Ejemplo de manual

Workers

Select one or more assigned workers. Each worker receives the same assignment.

☐ BBS DEMO - Jefe de crew

☐ BBS DEMO - Tecnico 1

☒ BBS DEMO - Tecnico 2

☐ BBS ROLE LAB External Technician

☐ BBS ROLE LAB Project Manager

☐ BBS ROLE LAB Supplier Coordinator

Enter dates and times in UTC. The worker agenda also shows times in UTC.

Start (UTC)

10/16/2026, 08:00 AM

End (UTC, optional)

10/16/2026, 10:00 AM

Planned hours (optional)

2.00

Site (optional)

Required expertise

Publish assignment

Actual PM publish form before saving the synthetic future assignment.

Publish a future plan without creating actual time

The screenshot displays the BBS Role Manual interface. On the left is a sidebar with navigation links: Dashboard, Projects, Approvals, Reports, SECONDARY, Time, Expenses, My Pay, Team, Planning (highlighted), Documents, Profile, Company Webmail, and Sign out. The main content area shows the 'Publish field assignment' form. At the top, there's a header with 'Online', 'Go to section', a search bar, a notification bell, 'Webmail', 'EN', and the user 'BBS ROLE LAB Project Manager'. The form has two main sections. The top section is for creating a new assignment, with fields for 'BBS DEMO - Tecnico 2' (selected), '10/16/2026, 08:00 AM' (start time), 'End (optional)' (10/16/2026, 10:00 AM), 'Planned minutes (optional)' (120), 'Site (optional)', and 'Required expertise'. Below these are 'Save assignment' and 'Cancel assignment' buttons. The bottom section is titled 'Publish field assignment' and includes a description: 'Publish a planned assignment for one or more assigned workers. Planning does not create actual time entries; each worker records the work performed separately.' It has a 'Project' dropdown set to 'C-0050-P-20261005 — BBS · Ejemplo de manual' and a 'Workers' section with three checkboxes: 'BBS DEMO - Jefe de crew', 'BBS DEMO - Tecnico 1', and 'BBS DEMO - Tecnico 2'.

Online Go to section %/Ctrl K

Webmail EN BBS ROLE LAB Project Manager Manager

BBS DEMO - Tecnico 2 10/16/2026, 08:00 AM

End (optional) 10/16/2026, 10:00 AM

Planned minutes (optional) 120

Site (optional)

Required expertise

Save assignment

Cancel assignment

Publish field assignment

Publish a planned assignment for one or more assigned workers. Planning does not create actual time entries; each worker records the work performed separately.

Project C-0050-P-20261005 — BBS · Ejemplo de manual

Workers Select one or more assigned workers. Each worker receives the same assignment.

☐ BBS DEMO - Jefe de crew

☐ BBS DEMO - Tecnico 1

☐ BBS DEMO - Tecnico 2

Actual PM published plan:120 minutes in UTC, independent of actual work.

Change a published assignment and verify persistence

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Planning → Published schedule → Open record

A published assignment can be edited through its own record. Updating the plan does not correct an actual source that a worker has already submitted.

Do the task

1. Open Published schedule and choose Open record for the correct BBS worker/date.
2. Inspect Worker, Start, End, Planned minutes, Site and Required expertise.
3. Change the intended planning value and choose Save assignment. Reopen the same record to verify the new value.
4. If the assignment should be canceled, use Cancel assignment on that record, then verify its state and tell the affected worker. Cancellation was inspected but not executed here, preserving the positive worker agenda example.

Verify the result

- PM changed only the fictional bench site note and Save assignment succeeded; the original worker, date and 2-hour plan remained.
- No October 16 actual time source was created by either publish or update.

If you get stuck

- Check that you opened a planning record, not a time-entry source. Actual submitted work requires the reviewed correction path.
- Coordinate a genuine cancellation with the worker; do not assume a changed plan deletes recorded history.

Change a published assignment and verify persistence

Online Go to section [W/Ctrl K](#) [Webmail](#) EN [BR](#) BBS ROLE LAB Project Manager Manager

C-0050-P-20261005 — BBS · Ejemplo de manual

Workers
Select one or more assigned workers. Each worker receives the same assignment.

- ☐ BBS DEMO - Jefe de crew
- ☐ BBS DEMO - Tecnico 1
- ☐ BBS DEMO - Tecnico 2
- ☐ BBS ROLE LAB Coordinator-recorded Technician
- ☐ BBS ROLE LAB External Technician
- ☐ BBS ROLE LAB Project Manager
- ☐ BBS ROLE LAB Supplier Coordinator

Enter dates and times in UTC. The worker agenda also shows times in UTC.

Start (UTC) End (UTC, optional)

Planned hours (optional) Site (optional)

Required expertise

[Publish assignment](#)

Success
Assignment updated.

Sign out

Actual PM Save assignment result after changing the fictional site note.

Follow a shared plan through crew work and review

Isolated BBS planning and crew lab · October 20–25, 2026. Browser-verified synthetic operational records; no real dispatch, payment or customer acceptance. Historical financial-course totals retain their original date scope.

Go here: Planning → October 20; Worker / Chief: Today; Approvals

The Owner published one common October 20 08:00–16:00 UTC plan to the Chief and two existing technicians. This created three planning records, one per person. Their separate Worker-role agendas each showed an eight-hour BBS plan. Project membership and dated chief delegation remained separate prerequisites.

Actual work differed: Technician 1 personally recorded six hours; the Chief recorded seven hours for Technician 2 through the delegated Crew workspace; the Chief personally recorded eight hours. Each source was submitted individually and reviewed by a separate Project Manager account. No colleague's compensation or customer pricing is needed for this operational handoff.

Do the task

1. Open Planning, choose October 20 and inspect the three BBS agenda records. Confirm project, worker, UTC interval and 480 planned minutes for each.
2. Ask each worker to check Today → Upcoming assignments using their own account. They do not accept or complete the plan with a task button; they record and report actual work separately.
3. For delegated crew entry, have the Chief check project, date and managed worker before saving individual actual hours. Avoid duplicating a crew-entered source through a worker's own time form.
4. Open Approvals for BBS and October 20. Review the submitted 6 / 7 / 8 hours and operational notes. Choose the supported Approve control for each truthful source.
5. Ask the workers to reopen Time → Week of 2026-10-19. Technician 1 shows Actual 6.00h, Expected 8.00h, Difference –2.00h and Needs note; Technician 2 shows 7.00h / 8.00h / –1.00h and Needs note; Chief shows 8.00h / 8.00h / 0.00h and Approved.

Verify the result

- Native multi-worker publication created no actual time. Later separately authored sources persisted Approved with 360 / 420 / 480 minutes and the correct creator identities.
- Needs note is a weekly comparison indicator for approved time differing from its expectation. The underlying source remains Approved. Explain the work difference in operational notes/reports; never force actual hours to match a target.

Follow a shared plan through crew work and review · continued

If you get stuck

- A chief's ability to record crew time does not automatically grant review authority. Ask the Owner to verify the separate review permission.
- If a worker reports a missing plan, compare today in UTC, project membership and the published plan date. If the actual source is wrong, use the correction chapter rather than editing planning.

Follow a shared plan through crew work and review

Tuesday, October 20, 2026

BBS DEMO - Jefe de crew · C-0050-P-20261005 · 480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 1 · C-0050-P-20261005 · 480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 2 · C-0050-P-20261005 · 480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

Owner-created shared BBS plan visible in the authorized planning agenda: one record per person, each 480 planned minutes.

Follow a shared plan through crew work and review

DAY	ACTUAL	EXPECTED	DIFFERENCE	CATEGORIES	STATUS
Mon 2026-10-19	0.00h	8.00h	-8.00h	—	—
Tue 2026-10-20	6.00h	8.00h	-2.00h	Regular time 6.00h	Needs note
Wed 2026-10-21	0.00h	8.00h	-8.00h	—	—
Thu 2026-10-22	0.00h	8.00h	-8.00h	—	—
Fri 2026-10-23	0.00h	8.00h	-8.00h	—	—
Sat 2026-10-24	0.00h	0.00h	0.00h	—	—
Sun 2026-10-25	0.00h	0.00h	0.00h	—	—
Actual	6.00h	40.00h	-34.00h	Regular time 6.00h	—

Separate Worker 1 view after PM review: six actual hours versus an eight-hour expectation. This operational table deliberately excludes all compensation estimates.

Follow a shared plan through crew work and review

October 2026

<
Today
>

Select a day to see its agenda. Times shown in UTC.

Mon	Tue	Wed	Thu	Fri	Sat	Sun
28 .	29 .	30 .	1 .	2 .	3 .	4 .
5 .	6 .	7 .	8 .	9 .	10 .	11 .
12 .	13 .	14 .	15 .	16 1	17 .	18 .
19 .	20 3	21 1	22 1	23 .	24 2	25 1
26 .	27 .	28 .	29 .	30 .	31 .	1 .
2 .	3 .	4 .	5 .	6 .	7 .	8 .

Tuesday, October 20, 2026

BBS DEMO - Jefe de crew · C-0050-P-20261005 · 480 min
Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 1 · C-0050-P-20261005 · 480 min
Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 2 · C-0050-P-20261005 · 480 min
Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

Actual Project Manager calendar at 768-pixel tablet width, with the three October 20 planning records.

Follow a shared plan through crew work and review

Tuesday, October 20, 2026

BBS DEMO - Jefe de crew · C-0050-P-20261005

· 480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 1 · C-0050-P-20261005 ·

480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 2 · C-0050-P-20261005 ·

480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

Actual Project Manager selected-day agenda at 390-pixel phone width. The three worker records display their UTC intervals and planned quantities.

Distinguish planned hours, expected hours and work goals

Isolated BBS planning and crew lab · October 20–25, 2026. Browser-verified synthetic operational records; no real dispatch, payment or customer acceptance. Historical financial-course totals retain their original date scope.

Go here: Planning; Worker: Today and Time; Owner: Projects → Expected Working Schedule

The Owner configures Expected Working Schedule through Projects → More actions. It has an effective date, IANA timezone and a minutes value for each weekday. The BBS lab's October 19 schedule is 480 minutes Monday–Friday and zero on weekends. This reference is separate from published planning and never creates actual work.

The October 21 practice plan was edited to three hours, 09:00–12:00 UTC. Worker 1 sees Planned: 3 h, while the Wednesday timesheet still expects 8.00h and records 0.00h until actual work is entered. Creation displays Planned hours; the edit form displays Planned minutes, so three hours is 180 minutes.

Planning and worker agendas display UTC. On October 20, 08:00–16:00 UTC means 10:00–18:00 Europe/Madrid or 04:00–12:00 America/New_York. Convert for the actual date, because daylight-saving changes can alter the offset.

There is no generic worker-goal Accept / Reject / Mark completed workflow. Use assignments for coordination, expected hours for comparison and Daily / Technical reports for actual progress and blockers. Project milestones are separate project checkpoints; ask the Owner or Finance to establish any financial milestone terms. This operational exercise creates no milestone charges.

After the earlier planning tables, the Owner added an explicitly synthetic October 23-only membership for Technician 1 in the existing fictional onboarding project. The later Worker weekly table shows Friday Expected and Difference as — because two own projects cover that day. Earlier screenshots still correctly show Friday eight hours and weekly forty before that extra assignment. No actual work was entered in the second project.

Do the task

1. Open an existing Published assignments record, edit the interval, Planned minutes and optional site, and choose Save assignment. Reopen it to verify persistence and ask the worker to reload Today.
2. To cancel a plan, identify the correct project, person and dates and choose Cancel assignment. Check the calendar and the worker's upcoming agenda. Cancellation does not erase or correct an actual-time source.
3. If Today has no plan but lists Your assigned projects, check whether the plan is future or has not been published. Membership alone does not publish a shift.

Distinguish planned hours, expected hours and work goals · continued

4. If the worker is unavailable in the publish form, ask the Owner to check active account status and project-assignment coverage for the selected interval. Supplier personnel with coverage ending October 31 are not eligible on November 1.
5. If Expected is —, ask the Owner to check membership and effective schedule dates. Zero is a valid target; — means unknown. Worker 1's September 28–30 precede their October 1 membership and therefore show unknown expectations.
6. If multiple projects cover the day, do not add their targets together yourself. The application leaves the expectation unknown where it lacks a single effective project/schedule. Resolve the planning allocation with the Owner; the later October 23 one-day second-assignment checkpoint demonstrates the unknown target.

Verify the result

- Native PM edit saved 180 minutes, updated UTC dates and site; the Worker agenda reflected those values after reload. The weekly expected eight hours did not change.
- A separate October 22 Worker 2 plan was cancelled natively and disappeared from the Worker agenda. Its retained record has cancelled status and no actual-time source was generated.
- The later separate Worker session showed October 23 Actual 0.00h / Expected — / Difference — while the main October 20 six actual and eight expected hours stayed unchanged. Counting a future own membership for ambiguity did not expose that project in the current selector or add actual records.

If you get stuck

- The External Technician profile has restricted Time / Expenses / Reports access and currently no internal Today agenda or Planning calendar, even when the Owner publishes a plan. Confirm its schedule through the authorized operational handoff.
- Operational screenshots and hours comparisons do not authorize access to client rates, loaded costs, margins or another person's pay. Route financial interpretation to Finance or the Owner.
- After a publish-field validation message, correct the highlighted field and recheck the retained person, UTC interval, planned quantity, Site and Required expertise before retrying.

Distinguish planned hours, expected hours and work goals

Published schedule

Published

BBS DEMO - Tecnico 1 · C-0050-P-20261005 · BBS · Ejemplo de manual

Start

2026-10-21 09:00 UTC

End (optional)

2026-10-21 12:00 UTC

Planned minutes (optional)

180 min

Site (optional)

BBS planning lab · updated PM practice bench

Open project →

PM published record reopened after editing: October 21 09:00–12:00 UTC, 180 planned minutes and the saved fictional site.

Project Manager · BBS operational course

45 / 71

Distinguish planned hours, expected hours and work goals

Upcoming assignments

Showing 2 of 2

Published assignments after today, in date order.

Oct 20, 2026 · 08:00 – 16:00 UTC

C-0050-P-20261005

BBS · Ejemplo de manual

BBS planning lab · fictional crew bench

Planned: 8 h

Open project →

Oct 21, 2026 · 09:00 – 12:00 UTC

C-0050-P-20261005

BBS · Ejemplo de manual

BBS planning lab · updated PM practice bench

Planned: 3 h

Open project →

Separate Worker 1 agenda after the edit: the published three-hour practice plan appears alongside the eight-hour crew plan.

Distinguish planned hours, expected hours and work goals

DAY	ACTUAL	EXPECTED	DIFFERENCE	CATEGORIES	STATUS
Mon 2026-10-19	0.00h	8.00h	-8.00h	—	—
Tue 2026-10-20	6.00h	8.00h	-2.00h	Regular time 6.00h	Needs note
Wed 2026-10-21	0.00h	8.00h	-8.00h	—	—
Thu 2026-10-22	0.00h	8.00h	-8.00h	—	—
Fri 2026-10-23	0.00h	8.00h	-8.00h	—	—
Sat 2026-10-24	0.00h	0.00h	0.00h	—	—
Sun 2026-10-25	0.00h	0.00h	0.00h	—	—
Actual	6.00h	40.00h	-34.00h	Regular time 6.00h	—

Separate Worker 1 weekly table: planned three hours does not replace the independently configured eight-hour Wednesday expectation. This crop contains no pay figures. This is the earlier checkpoint, before the additional October 23 one-day membership; its Friday eight-hour expectation and weekly forty-hour target remain correct for that saved stage.

Distinguish planned hours, expected hours and work goals

BBS DEMO - Tecnico 2 · C-0050-P-20261005 · 2026-10-22 12:00 → 2026-10-22 14:00

Worker

BBS DEMO - Tecnico 2

Start

10/22/2026, 12:00 PM

End (optional)

10/22/2026, 02:00 PM

Planned minutes (optional)

120

Site (optional)

BBS planning lab · cancel practice

Required expertise

Save assignment

Cancel assignment

Actual PM Cancel assignment control for the separate October 22 Worker 2 practice plan. Verify the worker and interval before cancelling.

Distinguish planned hours, expected hours and work goals

Thursday, October 22, 2026

BBS ROLE LAB External Technician · C-0050-P-20261005 · 120 min

Oct 22, 2026, 08:00 AM – Oct 22, 2026, 10:00 AM

October 22 agenda after cancellation: the Worker 2 practice plan has disappeared; the separate external-technician two-hour plan remains.

Distinguish planned hours, expected hours and work goals

DAY	ACTUAL	EXPECTED	DIFFERENCE	CATEGORIES	STATUS
Mon 2026-09-28	0.00h	—	—	—	—
Tue 2026-09-29	0.00h	—	—	—	—
Wed 2026-09-30	0.00h	—	—	—	—
Thu 2026-10-01	0.00h	8.00h	-8.00h	—	—
Fri 2026-10-02	8.00h	8.00h	0.00h	Regular time 8.00h	Approved
Sat 2026-10-03	3.00h	8.00h	-5.00h	Travel 3.00h	Needs note
Sun 2026-10-04	0.00h	0.00h	0.00h	—	—
Actual	11.00h	—	—	Regular time 8.00h - Travel 3.00h	—

Separate Worker 1 historical week: dashes before the October 1 assignment demonstrate an unknown expected target, rather than a zero-hour schedule.

Distinguish planned hours, expected hours and work goals

Published schedule

Published

BBS DEMO - Tecnico 1 · C-0050-P-20261005 · BBS · Ejemplo de manual

Start

2026-10-25 08:00 UTC

End (optional)

2026-10-25 10:00 UTC

Planned minutes (optional)

120 min

Site (optional)

BBS planning lab · preserved
PM site

Required expertise

BBS training PLC

Open project →

Additional PM October 25 practice publication reopened after correcting an invalid interval: saved UTC 08:00–10:00, 120 planned minutes, fictional Site and Required expertise. No actual work was generated.

Project Manager · BBS operational course

51 / 71

Distinguish planned hours, expected hours and work goals

DAY	ACTUAL	EXPECTED	DIFFERENCE	CATEGORIES	STATUS
Mon 2026-10-19	0.00h	8.00h	-8.00h	—	—
Tue 2026-10-20	6.00h	8.00h	-2.00h	Regular time 6.00h	Needs note
Wed 2026-10-21	0.00h	8.00h	-8.00h	—	—
Thu 2026-10-22	0.00h	8.00h	-8.00h	—	—
Fri 2026-10-23	0.00h	—	—	—	—
Sat 2026-10-24	0.00h	0.00h	0.00h	—	—
Sun 2026-10-25	0.00h	0.00h	0.00h	—	—
Actual	6.00h	—	—	Regular time 6.00h	—

Later isolated checkpoint, after an additional one-day project membership on October 23: Friday Actual is zero and Expected / Difference are unknown (—). October 20 remains six actual versus eight expected hours. Earlier weekly tables precede this added membership and correctly show Friday eight expected hours. This operational crop contains no prices, costs or compensation.

Maintain expertise and availability in the correct scope

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Profile → Expertise and availability

Profile lets the PM inspect authorized workforce expertise and availability without exposing other workers' compensation. Availability windows and Planning use UTC. Account security below the workforce profile concerns your own signed-in account.

The positive exercise saved only the fictional PM's own available October 16 08:00–10:00 UTC window. No other person's real availability was changed.

Do the task

1. Open Profile. Use Inspect worker and View worker profile to confirm whose workforce information is displayed.
2. Choose Add availability. Enter Starts and Ends in UTC, select Available/appropriate status, add the operational note, and choose Save availability.
3. Reopen Profile and inspect the availability window table and calendar day. Check person, dates, times and status.
4. For expertise, use Add expertise, select the appropriate existing skill and proficiency, save, and recheck the table. Skill editing was inspected, not executed in this packet.

Verify the result

- Native PM availability Save succeeded and the reopened table showed the exact fictional October 16 window.
- The separate planning record remained Worker 2's future assignment; availability alone did not publish a plan or create hours.

If you get stuck

- Before changing a workforce record verify the selected person; changing Inspect worker does not switch your authenticated account.
- If the required expertise is absent, ask the Owner to maintain the expertise catalog. Avoid using an unrelated skill as a placeholder.

Maintain expertise and availability in the correct scope

The screenshot displays the 'Profile and security' page in the J&A system. The left sidebar contains navigation links: Dashboard, Projects, Approvals, Reports, Time, Expenses, My Pay, Team, Planning, Documents, Profile (selected), and Company Webmail. The main content area is titled 'Profile and security' and includes a 'Print report' button and a search bar. The 'WORKFORCE PROFILE' section is active, showing 'Expertise and availability' management. It includes a 'Search team' input, an 'Inspect worker' dropdown menu (currently showing 'BBS ROLE LAB Project Manager · Project manager'), and a 'View worker profile' button. Below this is an 'Add expertise' button. A table section titled 'Scroll horizontally to review all columns.' has columns for 'EXPERTISE', 'PROFICIENCY', and 'VERIFIED', with a message 'No expertise recorded.' Below the table is an 'Availability calendar' section with an 'Add availability' button and a calendar view for 'October 2026' showing 'Today'.

Online Go to section [W/Ctrl K](#) Webmail EN BR BBS ROLE LAB Project Manager Manager

J&A / Profile and security [Print report](#) Search projects, people, invoices... [Search](#)

Profile and security

WORKFORCE PROFILE

Expertise and availability

Review the selected worker's expertise and availability without exposing compensation or client rates.

Search team Inspect worker

BBS ROLE LAB Project Manager · Project manager [View worker profile](#)

[Add expertise](#)

Scroll horizontally to review all columns.

EXPERTISE	PROFICIENCY	VERIFIED
No expertise recorded.		

Availability calendar
Choose a day to add availability. Open an existing window to edit it. Times are UTC.

[Add availability](#)

October 2026

Select a day to see its agenda. Times shown in UTC.

< Today >

Actual PM Profile: saved fictional availability window and own account security.

Record your own operational time and hand it off

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Time → Log time → Save draft → Submit

The PM can record personal operational work separately from reviewing crew facts. The Time register can include authorized people; your source must name the intended worker. My Pay remains personal.

The positive exercise saved 0.50 actual hour on October 8 for the fictional PM's documentation work, then submitted it. It remains pending another authorized reviewer; this packet did not self-approve it.

Do the task

1. Open Time, filter BBS and the intended dates, then choose Log time.
2. Select Assigned project BBS, enter the actual Date, Operational category, Actual hours and Activity summary. Add start/end times only if known.
3. Choose Save draft. Open the saved source and verify the person, date, duration and summary.
4. Choose Submit for the reviewed draft. Confirm Submitted and give its source to another authorized reviewer.
5. For weekly entry, inspect every draft included before Submit all week drafts. Copy previous week layout copies layout; it is not a statement that the work happened. Weekly copy/bulk submission were inspected, not executed in this PM packet.

Verify the result

- The PM source was genuinely saved and Submitted with 30 minutes.
- The source was not approved, financially classified or invoiced. Personal pay showed a pending estimate rather than proof of payment.

If you get stuck

- Correct an ordinary draft before submission. Once submitted, follow a returned linked correction and explicit resubmission.
- If finalized settlement or billing coverage blocks a correction, hand off to Finance/Owner with the exact error.

Record your own operational time and hand it off

J&A AUTOMATION

Log time

Operational entry only. Commercial rules are applied separately.

Worker

BBS ROLE LAB Project Manager — bbs-role-lab-manager@example.t

Capture actual work

Enter what happened on site, not its commercial interpretation.

Assigned project

C-0050-P-20261005 — BBS · Ejemplo de manual

Date

10/06/2026

Operational category

Work

☐ Add start and end times

Actual hours

Actual duration: —

Enter decimal hours, for example 7.5.

Activity summary

Time entries

Print report

Archived projects are hidden.

WORKER OPERATIONS

Time

Record actual operational time. Commercial interpretation is applied from configured project rules.

Log time

Save a draft while details are still changing. Submit time only after the recorded date, duration and accuracy are accurate; submitted time is reviewed and cannot be silently overwritten.

Actual recorded

0.00h

Hours recorded for the selected scope.

Needs attention

0

Draft or review state

WEEKLY TIMESHEET

Actual time, one week at a glance

2026-10-05 → 2026-10-11. Planning target only; it never creates time.

← Previous week This week Next week →

Actual PM Log time form for personal operational work.

Record your own operational time and hand it off

Online %/Ctrl K EN BBS ROLE LAB Project Manager Manager

Worker: All workers Client: All clients

From: 10/08/2026 To: 10/08/2026

Sort by: Newest first Category: All categories

Period: Today This week This month Last month

Active filters: 3 1 matching records

Project: C-0050-P-20261005 — BBS · Ejemplo de manual From: 2026-10-08 To: 2026-10-08

ACTIVITY REGISTER

Recent time entries 1

2026-10-08 · C-0050-P-20261005 Manage record →

Regular time · 0.50h · Submitted

SYNTHETIC ROLE LAB: project manager own operational documentation, no live dispatch.

Open record →

Success
Time submitted.

Developed by Álvaro Schwiedop Souto

Actual PM saved-and-submitted half-hour training source.

Inspect receipts and distinguish operational review from repayment

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Expenses → Record expense / Approvals Expenses

Expenses records receipt evidence and operational facts: project, date, category, vendor, currency, amount and who paid. The amount spent, customer recovery and worker reimbursement are separate decisions. The PM operationally approved existing synthetic receipts; PM own expense creation was not executed here.

Do the task

1. Open Expenses and filter BBS, date range, worker, category, currency or Receipt evidence as needed.
2. Open the receipt/source and check the event, amount, currency, payer and any linked logged hours. Required receipt missing needs supporting evidence before submission or review.
3. For your own permitted new expense choose Record expense, enter the factual fields and attach the receipt, then Save draft and inspect it before Submit. This is an inspected reference path in the PM packet.
4. For another submitted expense, go to Approvals → Expenses and Approve correct operational facts or return a specific Required change.
5. Send Finance the approved source for commercial classification and the later reimbursement/payment process.

Verify the result

- PM operational approvals succeeded for the fictional USD 12 worker supply receipt, USD 20 allocated shared meal and USD 8 external expense.
- No reimbursement date, payee, customer markup or actual payment was recorded by the PM packet.

If you get stuck

- Never change currency merely to make an amount resemble another view. Check receipt evidence and the actual original spending currency.
- An Approved receipt is not proof of reimbursement; the authorized Finance process and the worker's own payment status provide that check.

Inspect receipts and distinguish operational review from repayment



Dashboard

Projects

Approvals

Reports

SECONDARY

Time

Expenses

My Pay

Team

Planning

Documents

Profile

Company Webmail

Sign out

Online

Go to section: %/Ctrl K



Webmail

EN

BR

BBS ROLE LAB Project Manager

J&A / Expenses and receipts

Print report

Search projects, people, invoices...

Search

Archived projects are hidden.

Include archived projects

WORKER OPERATIONS

Expenses and reimbursements

Record the receipt and operational facts. Finance handles later classification.

+ Record expense

Weekly expense timesheet

Previous week

Next week

This week

Week containing

10/05/2026

Show week

2026-10-05 → 2026-10-11

Daily expenses by currency and approval status

Day	Expenses	Total	Status
2026-10-05	0	—	—
2026-10-06	0	—	—

Actual PM Expenses register: scoped operational source filters and receipt review.

Read only your own compensation and payment status

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: My Pay → From / Through → Apply period

My Pay is always limited to your signed-in account's activity, compensation and reimbursement. Reviewing another worker's operational record does not permit seeing their compensation.

Estimated compensation, approved compensation, finalized settlement, expected payment date and recorded actual payment mean different things. A settlement is not a bank transfer.

Do the task

1. Open My Pay and select From and Through; choose Apply period.
2. Review approved and pending estimates, Own activity detail, Settlement status and Reimbursement status for that period.
3. Compare the source state with the estimate. For the PM October 8 half-hour Submitted source, the October 1–31 view showed USD 30 pending estimate under the fictional USD 60/hour rule.
4. Use Generate report for your own worker statement if needed. Statement generation was not executed in this PM packet.
5. If an amount or expected payment is wrong, give Finance the source/project/period and the observed difference.

Verify the result

- Native My Pay opened. Even a URL query naming Worker 2 kept the PM's own 0.5-hour/ USD 30 pending scope; it exposed no other worker's compensation.
- The PM packet created no settlement or actual payment.

If you get stuck

- Check period first: the default view ended on the current day, excluding future October 8 training activity.
- Do not assume an estimate is money owed today or money received. Ask Finance about settlement and payment evidence separately.

Read only your own compensation and payment status

The screenshot displays the 'My Pay' section of the J&A system. The left sidebar contains navigation links: Dashboard, Projects, Approvals, Reports, SECONDARY (Time, Expenses, My Pay, Team, Planning, Documents, Profile), and Company Webmail. The main content area shows the 'My Pay' title with a 'Print report' button and a search bar. Below this is a date range selector for 'From' (10/01/2026) and 'Through' (10/31/2026) with an 'Apply period' button. A 'Worker statement' section includes a 'Generate report' button. Two summary cards show 'APPROVED COMPENSATION - USD' and 'APPROVED REIMBURSEMENTS - USD', both at \$0.00. The compensation card notes '0 approved minutes'. The reimbursement card shows 'Estimated compensation awaiting approval: \$30.00' and 'Estimated reimbursements awaiting approval: \$0.00'. A 'Payment still outstanding' section states that no reviewed payments or approved reimbursements are outstanding in this period.

Online Go to section %/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

J&A / My Pay

Print report Search projects, people, invoices... Search

From 10/01/2026 Through 10/31/2026 Apply period

Worker statement

Download your own activity, compensation, settlement, and reimbursement statement for this period. Generate report

APPROVED COMPENSATION - USD

\$0.00

0 approved minutes

APPROVED REIMBURSEMENTS - USD

\$0.00

Estimated compensation awaiting approval: \$30.00 -
Estimated reimbursements awaiting approval: \$0.00

Payment still outstanding

Reviewed compensation and approved expenses that have not been paid yet.

No reviewed payments or approved reimbursements are outstanding in this period.

Sign out

Actual PM My Pay: own pending USD 30 estimate despite another-worker query parameter.

Upload and retrieve private project evidence

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Documents → Register a private artifact

Private documents are authorized at access time and retained as evidence. A changed file is registered as a new document, preserving the original. Sensitivity must match the actual content; Internal is not the same as customer-ready.

The PM exercise uploaded a 187-byte UTF-8 file labelled SYNTHETIC TRAINING ONLY to BBS, then downloaded the native registered bytes.

Do the task

1. Open Documents and select BBS. Expand Register a private artifact.
2. Confirm the project, enter Artifact type and Description, select the correct Sensitivity, and choose the intended file.
3. Choose Upload and register hash. Check the new filename, project, type, size and available View/Download controls.
4. Use Download on the exact document. Confirm the returned file is the expected content, not an error page or another project's artifact.
5. For a correction upload a new file with a clear description. Archive only the intended document when authorized; archive mutation was not executed here.

Verify the result

- Native upload and Download succeeded as PM. Original and downloaded SHA-256 both equal 847e4e65d78b721f04fe089beb4edfe82b7440fc7046a02ca52bcd65c0d71934.
- Only the synthetic new document was added; existing private receipts and invoice masters were preserved.

If you get stuck

- If scanning or processing is pending, wait for the authorized artifact process and use its normal retry/status controls. Do not mark a file safe yourself or substitute a public link.
- If download is denied, check current project scope, document sensitivity/state and your account; give the Owner the document reference.

Upload and retrieve private project evidence

The screenshot displays the J&A Documents interface. On the left is a sidebar with navigation options: Dashboard, Projects, Approvals, Reports, SECONDARY (Time, Expenses, My Pay, Team, Planning), Documents (highlighted), and Profile. At the bottom of the sidebar is a 'Sign out' button. The top header shows 'Online', a 'Go to section' dropdown, a notification bell, 'Webmail', language 'EN', and the user 'BR BBS ROLE LAB Project Manager Manager'. The main content area is titled 'Documents' and includes a 'Print report' button and a search bar. A message states 'Archived projects are hidden.' with an 'Include archived projects' button. Below this is a 'Register a private artifact' section. The 'Private project documents' section lists two items: 'synthetic-crew-receipt.png' (34706 bytes) and 'synthetic-training-receipt.png' (34818 bytes). Each item has a 'View' button and a 'Download' button. The interface also features a search bar, a 'Sort by' dropdown set to 'Newest first', and a '3 files' indicator.

Actual PM Documents: BBS private receipt evidence before the new upload.

Upload and retrieve private project evidence

The screenshot displays the 'Documents' section of the J&A Automation BBS Role Lab Project Manager. The interface includes a left sidebar with navigation options: Dashboard, Projects, Approvals, Reports, SECONDARY (Time, Expenses, My Pay, Team, Planning, Documents, Profile), and Company Webmail. The main content area shows the 'Documents' page with a search bar, a 'Print report' button, and a 'Search' button. A message states 'Archived projects are hidden.' with an 'Include archived projects' button. Below this is a 'Register a private artifact' section. The 'Private project documents' section explains that registered documents are retained as evidence and provides instructions on uploading corrected files. It also notes that files are private, hash-verified, and authorized on every download. A search bar and a 'Sort by' dropdown (set to 'Newest first') are present. A list of documents is shown, including 'BBS-ROLE-LAB-PM-NOTE.txt' (C-0050-P-20261005 - SYNTHETIC TRAINING note - 187 bytes) and 'synthetic-crew-receipt.png'. Action buttons for 'View', 'Download', and 'Archive' are available for each document. A success message at the bottom right states: 'Success Private document uploaded and hash-registered.'

Actual PM result: synthetic UTF-8 training note registered with native Download.

Read notifications without confusing them with approvals

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Notifications → All / Unread

Notifications point to work requiring attention. Marking an item read is an inbox action; it does not approve a source, accept a customer report or pay a worker.

Do the task

1. Open Notifications through the navigation or More menu.
2. Use All or Unread and open the referenced record to understand what changed.
3. Perform the actual business action in Approvals, Reports or the relevant source page; return to the inbox afterward.
4. If a Mark read action is offered, use it only to clear the notification after reviewing it. The training PM inbox was empty, so no Mark read transition was claimed.


Verify the result

- Native PM Notifications loaded with zero records. This verifies the route and empty state, not delivery of every event type.

If you get stuck

- If a notification link is no longer accessible, give the Owner the record reference and current role. Do not use another account to bypass scope.
- Check the actual source state even when an inbox count is zero.

Read notifications without confusing them with approvals

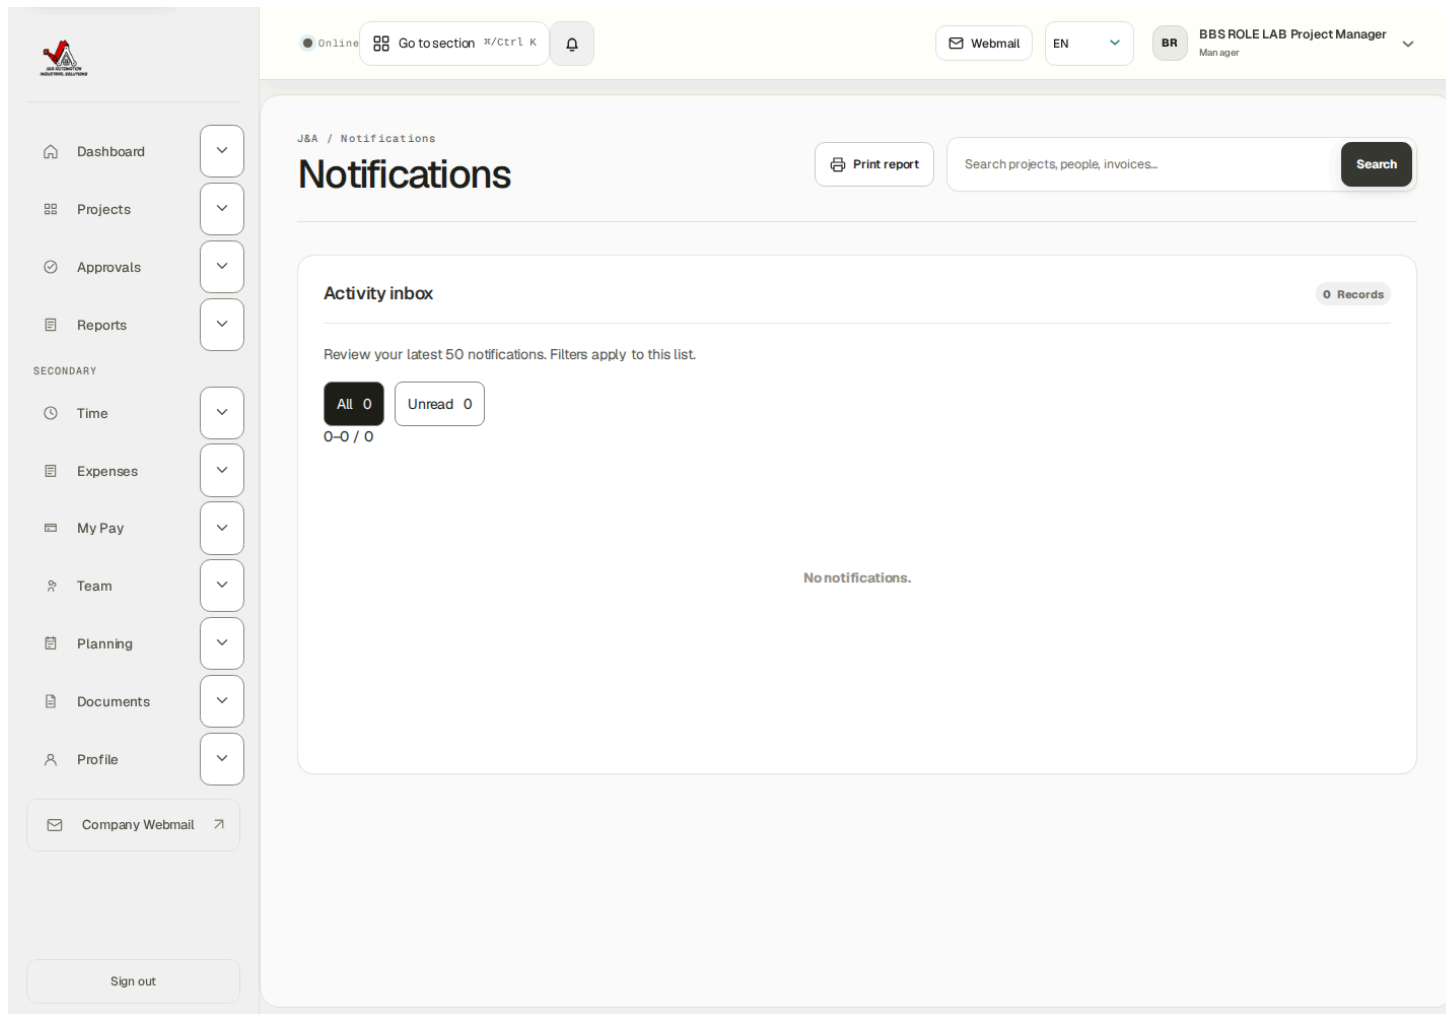

Actual PM inbox empty state; reading notifications is separate from business review.

Manage your account and find the correct guide

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Profile → Account security / Help

Profile security refers to your signed-in account. Passkeys and optional authenticator MFA require your own device and secure storage of recovery material. This packet inspected the controls without registering a device or exposing recovery codes.

Help identifies role-specific starting points and guide language. The screenshot reflects the catalog available during browser capture; publication of this new guide updates that reading path.

Do the task

1. Open Profile and verify your account email and Project manager role in Account security.
2. For a passkey, enter a descriptive Device name and choose Register passkey on your own supported device. Complete its device prompt and verify registration. This is a reference procedure, not an executed credential change.
3. For MFA, choose Enable MFA only when ready to complete the authenticator setup and securely store recovery codes. Never put the setup secret in a project report.
4. Open Help, choose the guide language and the Project Manager reading path. Use the Owner guide for delegated Owner prerequisites; do not treat Owner-only instructions as your own permissions.
5. Sign out when finished, especially on shared devices.

Verify the result

- Native PM Profile and Help loaded; workforce inspection did not switch the authenticated account.
- Finance and Audit direct routes returned 403 Access restricted; these actions remain outside the PM role.

If you get stuck

- For lost access or an incorrect role ask the Owner through the organization's approved contact path. There is no public sign-up.
- When reporting a UI error, include role, project reference, date range, record state, exact action and error text; exclude passwords, tokens and private customer data.

Manage your account and find the correct guide

The screenshot displays the 'Help and field guides' page within the J&A Automation BBS Role Lab Project Manager. The interface includes a left sidebar with navigation options: Dashboard, Projects, Approvals, Reports, and a 'SECONDARY' section with Time, Expenses, My Pay, Team, Planning, Documents, and Profile. A 'Company Webmail' link and a 'Sign out' button are also present. The main content area features a 'Back' button, the page title 'J&A AUTOMATION · BBS ROLE LAB PROJECT MANAGER', and the heading 'Help and field guides'. A 'Guide language' selector shows 'EN' as the active language. A key message states: 'Use the invitation linked to your mailbox. If your invitation is linked to a company mailbox, open it from that mailbox and sign in with the account it names. If you were invited as an external worker, use the single-use invitation link to create your account. There is no public sign-up.' Below this, a 'DETAILED REFERENCE' section for 'Work and projects guide' (Revision 2026-09-22) offers role-specific guidance for 'Worker' and 'Project manager'. It includes a 'Download PDF · EN' button and notes that available languages are EN and PT-BR. At the bottom, a section titled 'A normal day at a glance' provides four quick links: 'Record and submit time', 'Expenses and reimbursement', 'Your own compensation and payments', and 'Daily, technical and customer reports'.

Online Go to section: %/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

← Back

J&A AUTOMATION · BBS ROLE LAB PROJECT MANAGER

Help and field guides

Use these guides for the work you do in the portal. They show the real screen names and explain what each status means.

Guide language: EN ES PT-BR

Use the invitation linked to your mailbox

If your invitation is linked to a company mailbox, open it from that mailbox and sign in with the account it names. If you were invited as an external worker, use the single-use invitation link to create your account. There is no public sign-up.

DETAILED REFERENCE Revision 2026-09-22

Work and projects guide

Shared chapters for field work and project management; follow the path for your role.

Worker Project manager

This guide contains shared chapters. Read the sections for your role and its allowed tasks.

I am this role: where do I start?

Project manager: Start with assigned projects, then planning and operational review.

Download PDF · EN Available languages: EN, PT-BR

A normal day at a glance

Record and submit time → Choose Log time, the assigned project and the actual date and


Expenses and reimbursement → Record expense saves the

Your own compensation and payments → My Pay is always limited to

Daily, technical and customer reports → Daily records completed work,

Actual PM Help reading path and role-specific guidance.

Manage your account and find the correct guide

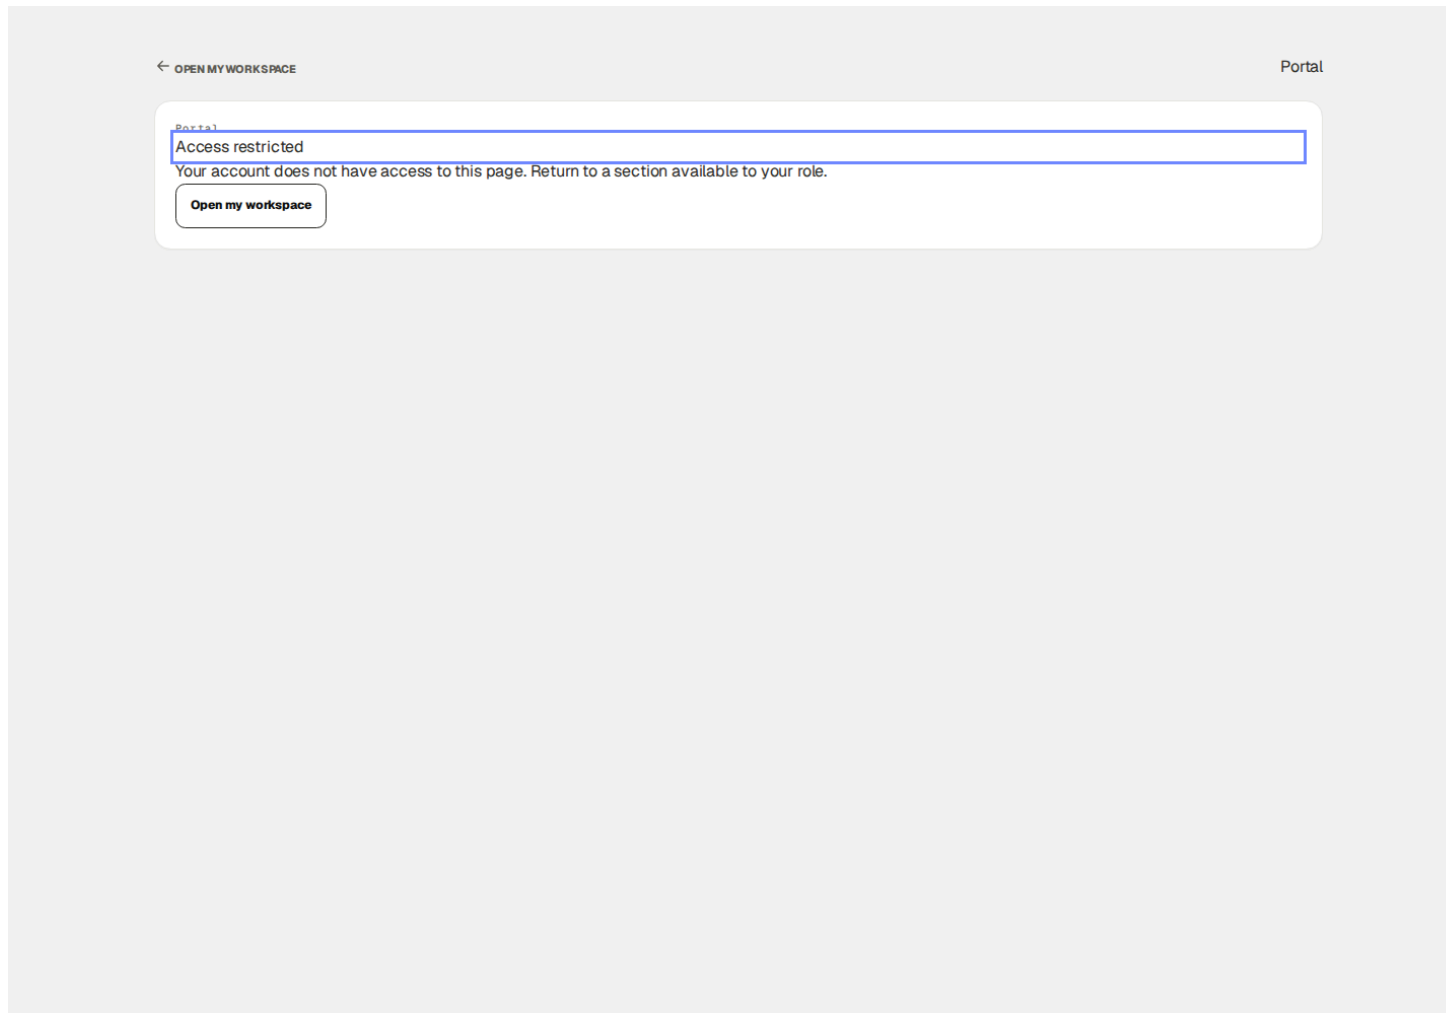

Actual PM 403 Access restricted for Finance: return to the operational workspace.

Complete the PM operational cycle and hand off

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Dashboard → Planning → Approvals → Reports

A practical PM day starts with authorized scope and future plans, moves through actual-source review and correction, and ends with report and finance handoffs. Finance remains responsible for commercial treatment and payment lifecycle; Owner remains responsible for company access and policy.

Coverage is explicit: browser-executed native approvals/returns, linked correction re-review, planning publish/update, own time submission, availability save, private document upload/download, scoped My Pay and navigation. Inspected reference controls include assignment edits/removal, own expense/report creation, plan cancellation, notifications read mutation, statement generation and device security enrollment.

Do the task

1. Confirm BBS project identity, timezone and your active membership. Check future Planning against availability.
2. Review submitted sources in the correct Approvals tab. Return incorrect facts with precise reasons and re-review submitted linked corrections.
3. Check approved Daily/Technical narratives and the exact customer period queue. Send Finance/Owner the approved source/period handoff.
4. Record personal work under your own source and send it to another reviewer. Check My Pay independently of crew economics.
5. Retain authorized project evidence, investigate processing/access errors, and report unresolved issues with exact source references.

Verify the result

- No live email, customer signature, dispatch, purchase, bank payment or production business mutation occurred in this training packet.
- The BBS original invoice and finalized compensation history remained unchanged.

Complete the PM operational cycle and hand off · continued

If you get stuck

- Do not solve a locked history problem by duplicating a project, time source or invoice. Use the supported correction or audited financial adjustment.
- When a task belongs to another role, send a clear handoff: source, project, period, state, required result and reason.
