

Project Manager · BBS operational course

Assigned projects, planning, operational review, corrections, reports and precise role handoffs

Actual role sessions · Exact controls · Saved outcomes · Recovery and handoffs

Project: BBS · Ejemplo de manual Number: C-0050-P-20261005

Read Before you practise before following any financial or operational training exercise. The training database is separate from the live portal.

Contents

Before practising · live and training access	3
Access · activate the invitation and sign in	4
Practice setup · your account and starting records	7
Review authority · who receives each source	8
Start with your account and assigned scope	9
Find the right workspace on desktop and phone	12
Use Dashboard to decide where to act	15
Inspect the project before changing its team	17
Assign workers and verify saved membership dates	19
Review a submitted source using the correct decision	23
Verify author recovery and approve the linked replacement	26
Review authored Daily and Technical facts with attribution	28
Review the ready customer version and acceptance queue	30
Publish a future plan without creating actual time	34
Change a published assignment and verify persistence	37
Follow a shared plan through crew work and review	39
Distinguish planned hours, expected hours and work goals	45
Maintain expertise and availability in the correct scope	56
Record your own operational time and hand it off	58
Inspect receipts and distinguish operational review from repayment	61
Read only your own compensation and payment status	63
Register and retrieve a private project document	65
Follow a notification to the current permitted source	68
Complete own reports and use the shared access/security procedures	71
Complete the PM operational cycle and hand off	74
Recovery · correct a source or request help	76
Security · verify your own device and recovery options	77
Completion check · your permitted role cycle	79

Before practising · live and training access

The company portal <https://j-aautomation.com/j-aautomation/app> is LIVE. A link to it never enters a simulation. For practice obtain a separately provisioned training URL, your own account, the permitted fictional project and dates, a visible environment identifier and the trainer's reset procedure. Without those, use this guide as a read-only demonstration and enter only authorized genuine work.

Original BBS examples include historical live-deployment records. Later training exercises used isolated copies. Each chapter identifies its dataset and checkpoint. Follow the dates and saved states shown for that exercise.

A role, project membership, review permission, supplier authorization and dated crew delegation are separate. Use your own credentials and follow the tasks assigned to your role. Check the selected project and person before recording work.

Verify the result

- Confirm your displayed identity, the environment, project number and work dates before saving. For training/reset or lost access contact admin@j-aautomation.com; send the route, role, project/record reference, time and visible error. Keep passwords, activation links, recovery codes and cookies private.

If you get stuck

- For an empty project selector, ask the Owner to check account status and assignment/authorization coverage. Do not create a duplicate project or borrow another account.

Access · activate the invitation and sign in

Go here: Your trusted invitation → Activate your account → Return to sign in → Profile

Do the task

1. Check the portal address and named account against the invitation provided by the Owner. There is no public sign-up. For an already provisioned account, use the sign-in method supplied to you; do not attempt to activate someone else's invitation.
2. For a single-use activation link, open Activate your account. Enter Full name and choose a Password of at least 12 characters, then Activate account. Wait for Account activated. You can sign in now. Do not repeatedly submit while Activating... is displayed.
3. Choose Return to sign in. Enter your account Email and Password and select Continue to workspace. If you previously enabled MFA, complete Verify your identity with the current Six-digit code and Verify and continue. Use a recovery code only through the offered Use a recovery code control.
4. Open Profile and verify the own-account name/email/role in Account security. Check the navigation and assigned project. A newly activated account can have zero assignments; activation alone does not grant project access or supplier/chief authority.

Verify the result

- The activation success message precedes the separate sign-in. Verify your own Profile and assigned projects after signing in.

If you get stuck

- An expired or already used link displays This invitation could not be activated. It may have expired or already been used. If activation already succeeded, return to sign in. Otherwise request a new invitation from the Owner; reloading does not renew the old link.
- For offline, temporarily unavailable or rate-limited activation, retain the entered name/password privately, restore connectivity or wait for the displayed retry interval, then retry. An unconfirmed response is not proof of an active account.
- For an incorrect password, inactive account or lost access, contact admin@j-aautomation.com from your verified account/contact channel. Supply identity and the visible error; never send the password. This guide does not promise a public password-reset form. The initial Owner is provisioned by the platform operator; an existing Owner provisions the remaining team.

Access · activate the invitation and sign in

J&A / INVITATION

Activate your account

Use a password of at least 12 characters. This invitation can be used once.

Full name Password Activate account

Account activated. You can sign in now.

[Return to sign in](#)

Isolated new recipient: the native activation success message. The password remains masked; this is separate from sign-in.

Access · activate the invitation and sign in

J&A / INVITATION

Activate your account

Use a password of at least 12 characters. This invitation can be used once.

Full name Password Activate account

This invitation could not be activated. It may have expired or already been used. Return to sign in if you activated it, or ask an owner for a new invitation.
[Return to sign in](#)

Reusing the same single-use training invitation shows the genuine recovery message. Return to sign in if already activated; otherwise request a new invitation.

Practice setup · your account and starting records

Obtain your own training account, isolated environment, authorized project and lesson dates from the trainer. Confirm the named starting records and expected result before saving. Ask the trainer to restore the checkpoint when needed.

Checkpoint	Required starting condition
Identity and environment	Own correctly provisioned role/profile; isolated URL and visible environment identity.
Project and dates	Exact project number, timezone and unused eligible lesson dates; membership and relevant grants cover both current access and the work date.
Source state	Named source IDs and durations/amounts; ordinary starting drafts/submissions; no unrelated correction already open.
Expected outcome	Expected saved state, source count, actual total and permitted output; named receiving reviewer where needed.

Verify the result

- Confirm that the visible starting records match this lesson. If they differ or an action is unavailable, stop and ask the trainer for the correct checkpoint.

Review authority · who receives each source

Review is determined by the source, base role and current dated grants. Chief delegation grants recording, not approval. A Worker with Can review checked does not become a Project Manager. Send a factual reason with every requested correction.

Source / recorder	Operational reviewer and prerequisite	Next handoff
Internal own or chief-delegated time	Owner or Finance; assigned PM with current active Can review membership for this project.	Submit the checked work to the authorized reviewer and verify the resulting state.
External/supplier time, including coordinator own time	Authorized Owner. Supplier authorization/recorder provenance keeps these sources outside the ordinary PM time queue.	Verify the resulting review state.
Own/delegated expenses	Owner or Finance; assigned PM with current project review grant. Check factual purchase, payer and evidence.	Verify the expense review state. Direct reimbursement questions to the Owner.
Daily and Technical reports, including supplier profiles	Owner or Finance; assigned PM with current project review grant and permitted project scope.	Owner/Finance prepares the customer period report and version-bound acceptance where required.
PM's own work	Route it to another authorized reviewer for an independent factual check. Do not infer a universal self-review prohibition solely from a job title.	Use the appropriate personal output and verify the review state.

If you get stuck

- If the intended source is absent, check source type, state, dates, assignment/review grant and supplier authorization before searching another queue. A review-enabled Worker Chief variant is not exposed by the current role model; Owner must provision the genuinely permitted reviewer role and grant. Never use a colleague's credentials to bypass this boundary.

Start with your account and assigned scope

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: [Sign in](#) → [Dashboard](#)

The Project Manager coordinates assigned projects and reviews operational facts. Account access, project membership, review permission and crew delegation are separate records. Having the Project Manager role does not automatically assign every project.

This guide uses the same saved BBS project as the Owner and other role guides. The fictional Project Manager account was created through Owner Team, signed in normally, assigned to BBS and granted Can review. The Owner completed the required dated project setup. Those setup actions belong to the Owner; this guide never asks you to create a duplicate BBS project.

Do the task

1. Use your own invitation or company account. Open the portal sign-in screen, enter the account email and password, and choose Continue to workspace.
2. Check that the account shown in Profile is yours and the role is Project manager. Never use the Owner or another worker's credentials to reach a missing control.
3. Open Dashboard and confirm BBS is in your authorized project scope. Open Projects and identify C-0050-P-20261005 before recording or reviewing anything.
4. Ask the Owner to verify active account status, dated project membership and Can review before starting this exercise. Assignment coverage must include the work date; current access also depends on the current application date.

Verify the result

- Native login succeeded as the fictional Project Manager. Dashboard showed one authorized active project after the Owner completed dated membership.
- An assignment starting the following UTC day initially showed no current project. The Owner added genuine coverage for the current day through native controls; no role or session was fabricated.


If you get stuck

- If BBS is missing, stop recording and give the Owner the project reference, your account and intended work dates. Do not create a replacement project.

Start with your account and assigned scope · continued

- If a review control is missing, check membership dates and Can review separately from the role label.

Start with your account and assigned scope

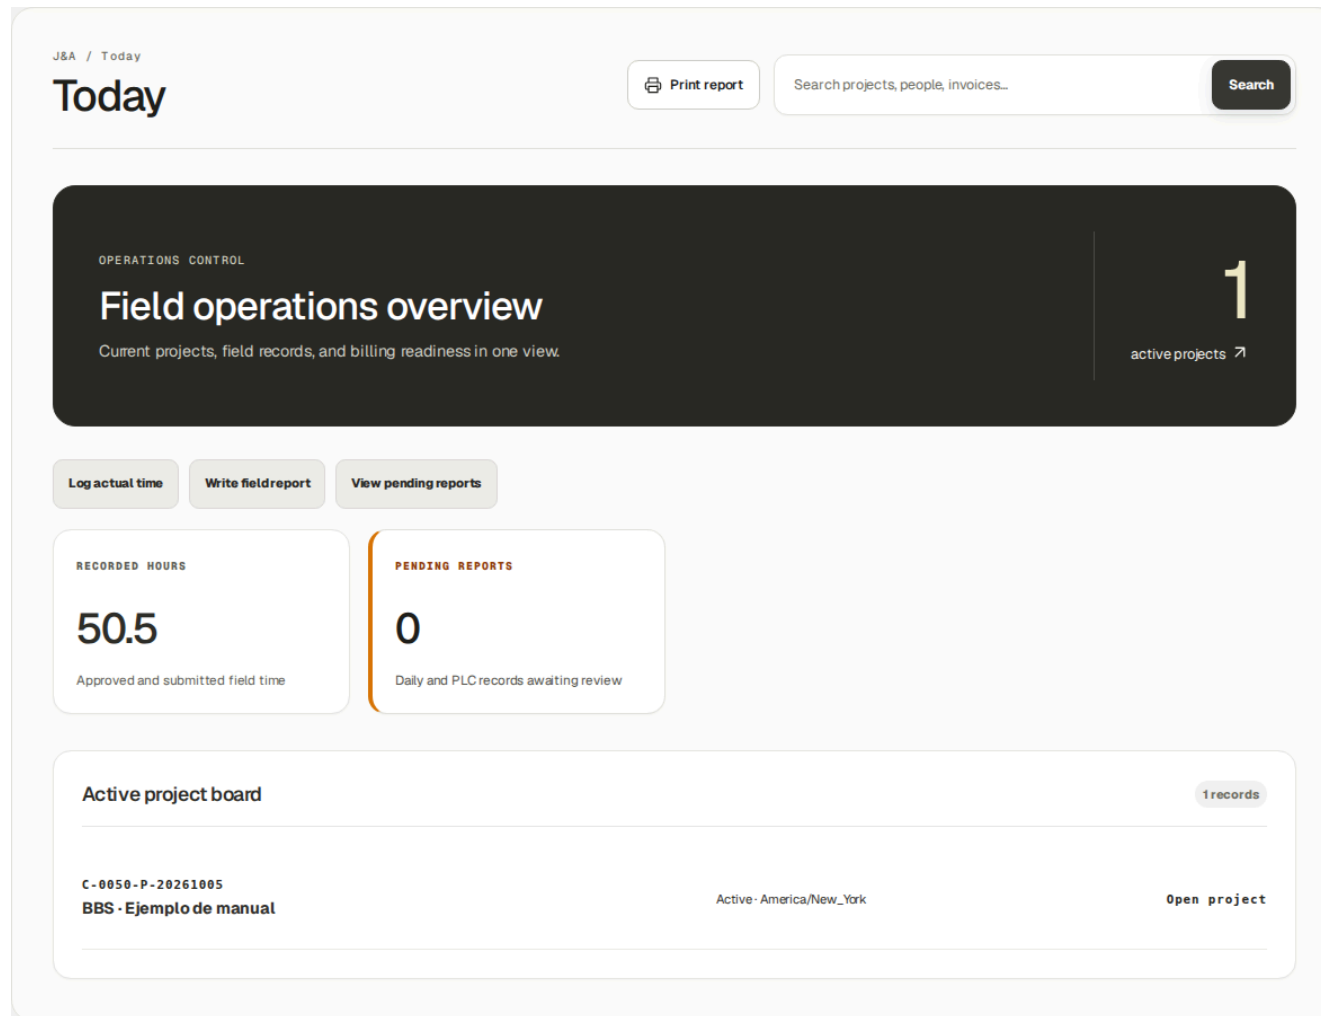

Actual Project Manager session: one authorized BBS project after native Owner onboarding.

Find the right workspace on desktop and phone

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Dashboard → primary navigation / More

Dashboard highlights operational activity. Projects holds project identity and scope; Approvals is the actionable review queue; Reports holds Daily, Technical / PLC and customer-follow-up views.

Time and Expenses are source registers. My Pay always concerns your own compensation. Team here is the operational directory and assignments, not Owner account administration. Planning publishes future assignments. Documents holds private project files; Profile holds expertise, availability and your security settings. Notifications and Help are separate destinations.

Do the task

1. On desktop select the named workspace in the sidebar. Keep the BBS project filter when changing registers.
2. On a phone use Dashboard, Projects, Approvals and Reports in the bottom navigation. Open More for the secondary workspaces.
3. Use the workspace filters rather than assuming every total concerns your own work. Time can show people across authorized projects; My Pay remains personal.
4. Use horizontal scrolling where the screen says Scroll horizontally to review all columns. Open a record to see its full facts before taking action.


Verify the result

- Actual PM navigation and Approvals were opened at 1440 desktop and 390 phone widths; the More drawer was captured.
- Planning was opened at 768 tablet width. These checks verify navigation and visible controls, not every device or browser.

If you get stuck

- If a drawer covers your content, close it or select a destination. Recheck the project and dates after navigation.
- Access restricted means the role cannot use that destination; return through Open my workspace and ask the Owner about the business handoff.

Find the right workspace on desktop and phone

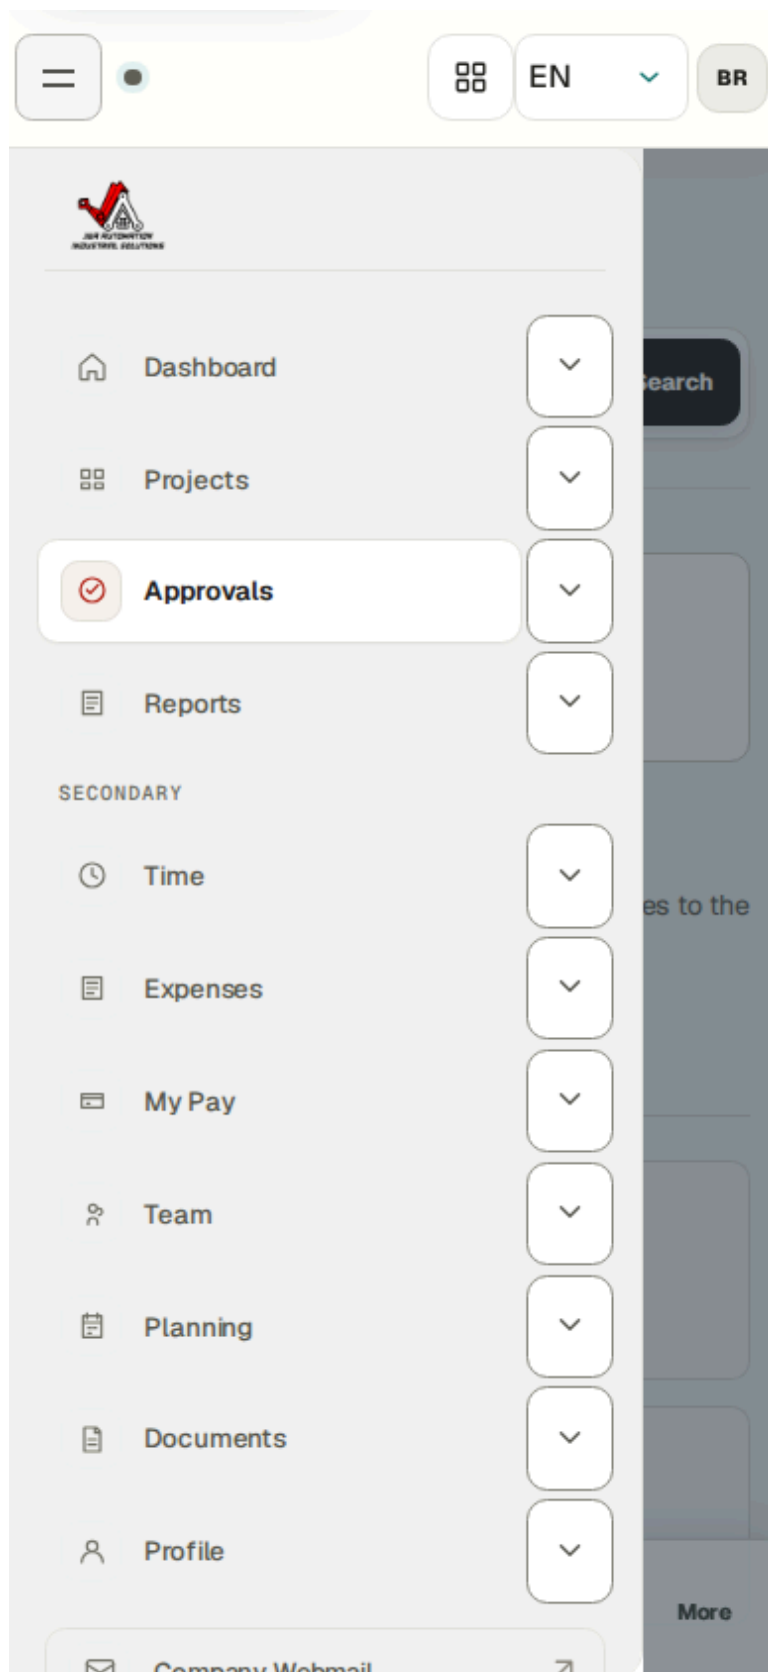

Actual PM phone session: More exposes secondary workspaces.

Find the right workspace on desktop and phone

≡

● Online

☰

🔔

✉ Webmail

EN ▼

BR

BBS ROLE LAB Project ...
Manager ▼

J&A / Resource planning

Resource planning

🖨 Print report

Search projects, people, invoices...

Search

Archived projects are hidden.

Include archived projects

October 2026

< Today >

Select a day to see its agenda. Times shown in UTC.

Mon	Tue	Wed	Thu	Fri	Sat	Sun
28 .	29 .	30 .	1 .	2 .	3 .	4 .
5 .	6 .	7 .	8 .	9 .	10 .	11 .
12 .	13 .	14 .	15 .	16 1	17 .	18 .
19 .	20 .	21 .	22 .	23 .	24 .	25 .
26 .	27 .	28 .	29 .	30 .	31 .	1 .
2 .	3 .	4 .	5 .	6 .	7 .	8 .

Monday, October 5, 2026

No events on this day.

Calendar times are shown in UTC. Planning never creates actual hours.

Published assignments

BBS DEMO - Tecnico 2 · C-0050-P-20261005 · 2026-10-16 08:00 → 2026-10-16 10:00

▼

Actual PM tablet session: BBS planning calendar.

Use Dashboard to decide where to act

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Dashboard → authorized project

Dashboard provides operational oversight. Recorded hours and activity counts describe the displayed operational scope. Open the underlying register to inspect its dates and state.

Do the task

1. Open Dashboard and identify the BBS project card and visible operational totals.
2. Choose the project or workspace behind an attention item. In Approvals use the BBS project and the work-date range to isolate the pending source.
3. Inspect the record and its history before deciding whether the facts are complete. Review daily work, expenses and reports in their own queues.


Verify the result

- The fictional PM dashboard displayed only authorized BBS project oversight.
- A cleared queue is a completion check; it does not replace inspecting an actionable record first.

If you get stuck

- If the number differs from a register, compare date range, workers, state filters and whether the dashboard figure means recorded or reviewed activity.
- Escalate questions outside the displayed operational scope to the Owner with the relevant project and source IDs.

Use Dashboard to decide where to act

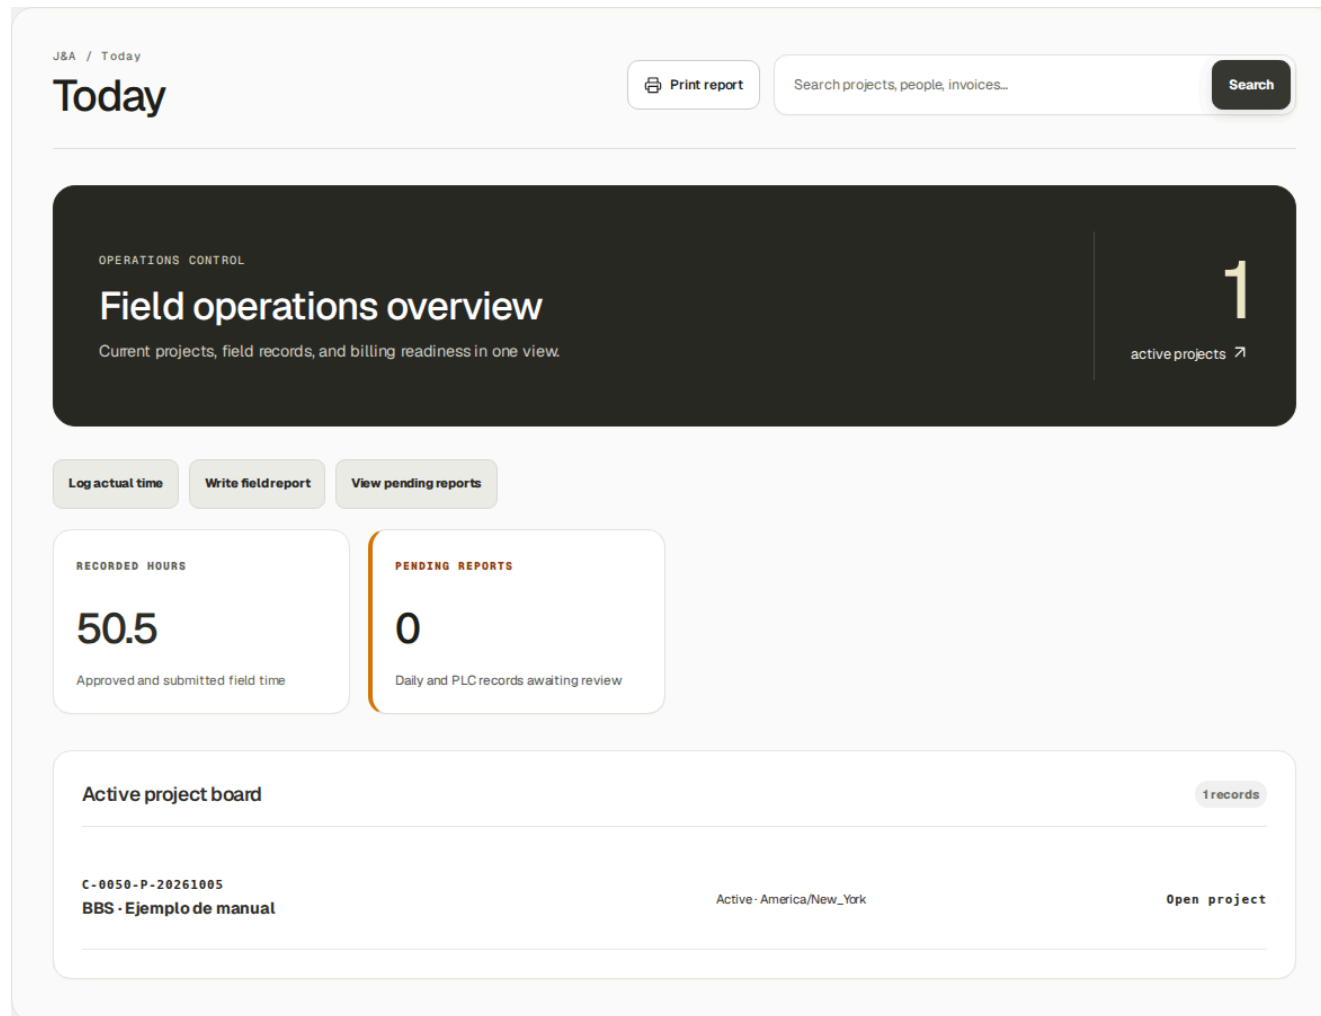

Actual PM Dashboard: operational oversight of the BBS training project.

Inspect the project before changing its team

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Projects → BBS → Overview

Project identity includes reference, client, status, schedule and timezone. BBS uses America/New_York for source work context, while Planning explicitly uses UTC. Your project Overview, Team and Reports / files views expose operational information.

Do the task

1. Open Projects. Use Search projects or Status, then Apply filters to find C-0050-P-20261005.
2. Open BBS and confirm the client, active status, planned start and timezone in Overview.
3. Open Team to inspect who is assigned and use Reports / files to reach project outputs and evidence.
4. Before making an assignment change, compare the intended work dates with existing coverage and the worker's availability.

Verify the result

- Native PM project detail and Team were opened. The project was scoped to BBS.
- Existing BBS records were preserved; this PM packet created no duplicate project.

If you get stuck

- Include archived projects only when looking for historical work. Do not reopen or duplicate archived work to circumvent a blocked source.
- Seek the Owner's handoff for project closing or other actions unavailable in your authorized workspace.

Inspect the project before changing its team

The screenshot displays the BBS Project Manager interface. At the top, there's a navigation bar with 'Online', 'Go to section', and a notification bell. The user is logged in as 'BBS ROLE LAB Project Manager'. The main header shows the project ID 'C-0050 · C-0050-P-20261005' and the project name 'BBS · Ejemplo de manual' with an 'Active' status. Below this, three summary cards show 'ACTUAL TIME' (88.50h), 'ASSIGNED TEAM' (7), and 'REPORTS' (12). The 'Overview' tab is selected, showing 'PROJECT CONTEXT' and 'OPERATIONS'. The 'PROJECT CONTEXT' section includes details like Client (BBS DEMO - Manual), Project Number (C-0050-P-20261005), PO / Reference (Not configured), Timezone (America/New_York), Client Number (C-0050), Cost Center (BBS-DEMO-20261005), Site / Plant (Not configured), and Schedule (2026-10-01). The 'OPERATIONS' section, titled 'Operational expenses', lists five items with their dates, descriptions, and amounts: SYNTHETIC TRAINING vendor (USD 6.50), BBS LAB fictional external tools (USD 8.00), BBS LAB fictional crew meal (USD 20.00), BBS LAB fictional supplies (USD 12.00), and Ferreteria ficticia DEMO (USD 50.00).

Online Go to section Ⓜ/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

Project report

C-0050 · C-0050-P-20261005 Active

BBS · Ejemplo de manual

BBS DEMO - Manual - - -

ACTUAL TIME 88.50h Recorded operational time

ASSIGNED TEAM 7 Current project assignment(s)

REPORTS 12 Daily and technical records

Overview Team Reports & Files

PROJECT CONTEXT Overview Active

CLIENT BBS DEMO - Manual CLIENT NUMBER C-0050

PROJECT NUMBER C-0050-P-20261005 COST CENTER BBS-DEMO-20261005

PO / REFERENCE Not configured SITE / PLANT Not configured

TIMEZONE America/New_York SCHEDULE 2026-10-01 → -

PROYECTO DE DEMOSTRACION. Equipo, horas y gastos ficticios para el manual. No facturar ni pagar realmente.

OPERATIONS Operational expenses 8

Reported expense amounts, receipt evidence and operational review state.

Filter by category All categories

E SYNTHETIC TRAINING vendor 2026-10-16 · Project materials · Submitted USD 6.50

E BBS LAB fictional external tools 2026-10-07 · Tools / consumables · Approved USD 8.00

E BBS LAB fictional crew meal 2026-10-06 · Meals · Approved USD 20.00

E BBS LAB fictional supplies 2026-10-06 · Tools / consumables · Approved USD 12.00

E Ferreteria ficticia DEMO 2026-10-03 · Tools / consumables · Approved USD 50.00

View all expenses →

Current scoped PM project overview, including operational source facts.

Assign workers and verify saved membership dates

Native isolated BBS role exercise · C-0050-P-20261005 · synthetic October 2026 work only

Go here: Team / Projects → assignments

Project membership and Can review are separate permissions. Assign only people whose work and dated coverage are authorized; the Owner completes the required project setup.

Do the task

1. Inspect the project and current membership dates. To add membership, open Assign worker and use Project, Expertise filter, Search workers, Worker, Starts on and optional Ends on, then Assign.
2. For an existing membership, open Update assignment, inspect Starts on and Ends on, choose Update and reload the membership to verify persistence.
3. The native exercise updated Worker 2's BBS membership from October 1/open-ended to October 1–31, verified the saved dates, then restored the open end through Update and verified it again.

Verify the result

- Update assignment was executed successfully and restored. Assign worker fields were inspected; a new assignment was not executed because available people already had overlapping membership.
- Native supplier membership date changes were rejected by the dated coverage guard. The attempted changes did not save. Ask the Owner to resolve coverage.

If you get stuck

- If a date change is blocked, read the validation and check saved membership before retrying. Do not bypass the guard or assume a directory record is membership.

Assign workers and verify saved membership dates

Starts on

10/01/2026



Ends on

10/31/2026



Update assignment

Actual existing-worker Update assignment form before saving the test end date.

Assign workers and verify saved membership dates

Starts on

10/01/2026



Ends on

10/31/2026



Update assignment

Reloaded membership with the saved October 31 end date.

Assign workers and verify saved membership dates

Starts on

10/01/2026



Ends on

mm/dd/yyyy



Update assignment

Final verified restoration of the original open-ended membership.

Review a submitted source using the correct decision

Native isolated BBS role exercise · C-0050-P-20261005 · synthetic October 2026 work only

Go here: Approvals → submitted source

Open the source and inspect author, project/date, duration or receipt, work facts and existing history. Review authority is source-specific. Supplier technician time is Owner-only; authorized PM operational report review is separate. See Review authority · who receives each source (review-authority) and Recovery · correct a source or request help (recovery-matrix).

Approve accepts the submitted operational facts. Needs changes requests a linked corrected draft while preserving the source. Reject records that the source is rejected; it is not the normal correction route.

Do the task

1. Choose Needs changes when the activity occurred but facts need correction. Enter a clear actionable reason, then verify Needs changes on the source.
2. Choose Reject for a source that should not count as submitted work, and record the reason. Reopen it to verify Rejected.
3. In the October 17 exercise PM rejected the fictional duplicate 15-minute source 01a11182-241b-74a7-8ad1-fc97a79e39ee. PM returned the separate 30-minute source 01a11182-2cc0-7526-9344-32c28151b219 because actual duration was 15 minutes.

Verify the result

- Both native decisions persisted on their exact sources. Needs changes permitted author correction; Rejected did not expose Create corrected draft.

If you get stuck

- A worker should read a rejection reason and avoid re-entering the rejected duplicate. If rejection was mistaken, escalate to the reviewer/Owner; do not promise a correction action absent from the source.

Review a submitted source using the correct decision

Online

Go to section [#/ctrl k](#)

Webmail

EN

BR

BBS ROLE LAB Project Manager
Manager

TIME ENTRY · SOURCE RECORD

Rejected

C-0050-P-20261005 · 2026-10-17

BBS · Ejemplo de manual · BBS DEMO - Tecnico 2

ACTUAL TIME

0.25 h

CATEGORY

Regular time

SITE

—

Activity summary

No code

SYNTHETIC PM02 reject exercise: duplicated fictional activity, no actual work asserted.

PROJECT TIMEZONE	SHIFT WINDOW	BREAK
America/New_York	— → —	—
SUBMITTED	APPROVED	
6 Oct 2026, 09:58 GMT-4	Not approved	

Review outcome

Review reason: SYNTHETIC PM02: reject duplicate fictional work; do not record it again.
This record was rejected. Contact the reviewer or Owner before recording replacement work.

Related reports

No related reports yet.
[View project reports](#)

Actual historical PM Reject result on the October 17 source. The preserved rejection and its factual reason are distinct from Needs changes.

Review a submitted source using the correct decision

Online

Go to section [#/ctrl k](#)

Webmail

EN

BR

BBS ROLE LAB Project Manager
Manager

TIME ENTRY · SOURCE RECORD

Needs changes

C-0050-P-20261005 · 2026-10-17

BBS · Ejemplo de manual · BBS DEMO - Tecnico 2

ACTUAL TIME

CATEGORY

SITE

0.5 h

Regular time

—

Activity summary

No code

SYNTHETIC PM02 Needs changes exercise: fictional documentation duration.

PROJECT TIMEZONE

SHIFT WINDOW

BREAK

America/New_York

— → —

—

SUBMITTED

APPROVED

6 Oct 2026, 09:58 GMT-4

Not approved

An existing correction is

Approved.

Open existing correction →

Review outcome

Review reason: SYNTHETIC PM02: actual documentation duration 0.25h; create linked correction.

Related reports

No related reports yet.

View project reports

Actual historical Needs changes source and its factual correction reason, with the current linked replacement preserved.

Verify author recovery and approve the linked replacement

Native isolated BBS role exercise · C-0050-P-20261005 · synthetic October 2026 work only

Go here: Returned source → linked correction → review

Needs changes is an author-recovery workflow. The recorded worker creates the linked corrected draft and submits it; PM verifies the replacement against the reviewer reason.

Rejected history is preserved separately and does not offer the same author correction action. See Review authority · who receives each source (review-authority) and Recovery · correct a source or request help (recovery-matrix).

Do the task

1. Open the returned October 17 Worker 2 source and verify the reason requests 15 actual minutes.
2. The worker opens Create corrected draft, enters the corrected duration/activity/reason, saves and submits the linked replacement.
3. PM opens replacement 01a11183-46a0-743e-92fc-e0760db21f77, compares the original link and reason, then Approves and reopens the saved source.

Verify the result

- The native author recovery and PM review were completed. Replacement is Approved at 15 minutes; original remains Needs changes. No duplicate rejected activity was recreated.

If you get stuck

- When a replacement does not address the reason, return it with specific remaining facts. Preserve all original/replacement links.

Verify author recovery and approve the linked replacement

Online

Go to section [#/ctrl k](#)

Webmail

EN

BR

BBS ROLE LAB Project Manager
Manager

TIME ENTRY · SOURCE RECORD

Approved

C-0050-P-20261005 · 2026-10-17

BBS · Ejemplo de manual · BBS DEMO - Tecnico 2

Corrected time entry

Correction reason: SYNTHETIC PM02 comply with PM returned actual-duration review.
Open original time entry →

ACTUAL TIME

0.25 h

CATEGORY

Regular time

SITE

—

Activity summary

No code

SYNTHETIC PM02 corrected Worker2 documentation0.25h.

PROJECT TIMEZONE

SHIFT WINDOW

BREAK

America/New_York

— → —

—

SUBMITTED

APPROVED

6 Oct 2026, 10:00 GMT-4

6 Oct 2026, 10:00 GMT-4

This record cannot be changed here. Contact the project owner or designated administrator.

Related reports

No related reports yet.
[View project reports](#)

Current Approved linked replacement: 15 actual minutes with the original retained; the operational review state is shown.

Review authored Daily and Technical facts with attribution

Native isolated BBS role exercise · C-0050-P-20261005 · synthetic October 2026 work only

Go here: Reports → source record

Daily and Technical reviews accept operational narratives. They do not approve supplier time, authorize customer acceptance or certify a clean attachment scan.

Work performed by, Report created by and Reviewed by identify distinct responsibilities. Verify the actual attribution after review.

Do the task

1. Open the submitted report and inspect project/date, narrative, evidence metadata and source version.
2. For Technical / PLC inspect context, diagnosis/change, validation result, production impact, risks and rollback. Read the saved native preview.
3. Use Approve or Needs changes with a reason as appropriate. Reopen the source and inspect Approved, reviewer, author and version.

Verify the result

- Native coordinator Technical source 01a1117d-a645-738f-adae-f60c4e5a3f4a reached Approved v3. Work performed by and Report created by show the coordinator; Reviewed by shows the PM. The October 13 coordinator Daily was also approved.

If you get stuck

- Check a private attachment's exact Storage and Scan status; Saved/Not scanned is not proof of clean scanning.

Review authored Daily and Technical facts with attribution

Report summary

PROJECT C-0050-P-20261005 BBS · Ejemplo de manual	WORK PERFORMED BY BBS ROLE LAB Supplier Coordinator bbs-role-lab-coordinator@example.test	REPORT CREATED BY BBS ROLE LAB Supplier Coordinator bbs-role-lab-coordinator@example.test	REVIEWED BY BBS ROLE LAB Project Manager bbs-role-lab-manager@example.test
SAFETY No safety flag Recorded with the source	Report version 3 2026-10-06T13:54:33.024Z		

Actual Approved Technical attribution: coordinator author and PM reviewer.

Review the ready customer version and acceptance queue

Native isolated BBS role exercise · C-0050-P-20261005 · synthetic October 2026 work only

Go here: Reports → customer period report → Customer follow-up

Approved time and reports are period inputs. Finance or Owner refreshes period reports and creates the customer artifact. PM then reads the exact customer version permitted by project scope.

The October 13–19 customer snapshot is v2 with content hash 85ba28d58be5c1f0c582266794df84fc491344508b23c63a33659b0ce98d6042. It contains the approved period inputs present at generation, including the coordinator Daily and 3.75 internal time hours displayed as 3.8 h. Later records do not silently rewrite this snapshot.

Do the task

1. After Finance prepares the period, open the Ready customer report PDF and inspect period, project, source identity, version and activity content.
2. For report 01a11179-da79-7298-baa2-074d02192e78 PM used the native Approve customer report action bound to that exact v2/hash.
3. Open the customer follow-up/acceptance queue for BBS, From October 13 to To October 19. Verify the row is Ready for signature and open the exact current report.
4. Hand the version to the authorized customer process. Record actual acceptance only when it occurs; a Ready for signature row is not a signed copy.

Verify the result

- Native Finance generation, PM exact-version approval and the Ready acceptance queue were verified. No customer signature, acceptance event or payment was invented. PM saw the approved operational hours and activity.

If you get stuck

- If later source corrections affect the period, ask Finance/Owner to create and review the new current version before requesting acceptance.

Review the ready customer version and acceptance queue

Dashboard

Projects

Approvals

Reports

SECRETARY

Time

Expenses

My Pay

Team

Planning

Documents

Profile

Company Website

Signal

SEARCH

On transaction: 10/01/21

INTERNAL

ON

BBSROLE LAB Project Manager

← Back

PRINT REPORT

BBS · Ejemplo de manual

OPERATIONAL RECORDS · REVIEW REQUIRED

Download PDF

Document preview

This preview reflects saved data. For authorized source records to change its content.

Actual data

J&A AUTOMATION

BBSROLE LAB

Project Period Report

Template: 2026-01-01

© 2026 J&A AUTOMATION · BBSROLE LAB · Ejemplo de manual · Oct 15, 2026 - Oct 15, 2026

OPERATIONAL RECORD

Project

C-0050-P-20260005-BBS-Ejemplo de manual

Client

BBS DEMO - Manual

Approved hours

3.8 h

Source records daily 1 Technical 0 Dispatch 0 Time 0

TIME	DATE	WORKER	ACTIVITY	HOURS	STATUS
Daily report	Oct 15, 2026	BBS ROLE LAB Supplier Coordinator	SYNTHETIC RECORDS: SCOD coordinate own documentation hardware to be dispatch	—	Approved
Time	Oct 15, 2026	BBS DEMO - Técnico 1	BBS ROLE GUIDE - workshop individual crew travel correction service	0.5 h	Approved
Time	Oct 15, 2026	BBS DEMO - Técnico 2	BBS ROLE GUIDE - Workshop clean own travel correction hardware period	2.5 h	Approved
Time	Oct 15, 2026	BBS DEMO - Técnico 2	BBS ROLE GUIDE - workshop individual crew travel correction service	0.8 h	Approved
Total				3.8 h	

Client Representative Signature

Name & Title

Date

Calculated values link to their source records. After changing an authorized source, recalculate the reports to create a new version approved and signed version preserve their history.

Reports / 3.8 hours 3.8 h 4 h

Customer signed copy evidence

A verified signed PDF copy is required for this report version to contain financial information.

Approve customer report

Approve the operational hours and activity in this immovable report snapshot. Customer conformity remains a responsibility.

Review customer report

Ready report

A finalized customer-ready report and a ready PDF are required before customer sign-off can be captured.

Generate report ready (Daily 0 Technical 0 PLC 0 Time entries)

Dispatch report

Preview customer-ready PDF

Only approved hours and activities are included

Reports / BBS ROLE LAB / PROJECT DATA / FOLLOW-UP

Operational follow-up

Events are added only, private to staff and bound to the exact report version and hash shown here.

Exact version and hash string: c2-855a78050e5c176c0c228c794f705f6e013445082263d3a353550a0a0808057

No follow-up events have been recorded.

Full follow-up history (3)

This record what staff (3.8 h) is not signature evidence and does not grant approval permission.

Event type Required

Dispatch method Required

Dispatch date Required

Dispatch reference Required

Named signatory

Reason

Next follow-up date

Record event

Approved hours

3.8 h

Daily reports

2026-10-13

SYNTHETIC RECORDS: SCOD coordinate own documentation hardware to be dispatch

Time entries

2026-10-15 Travel

BBS DEMO - Técnico 1 BBS ROLE GUIDE - synthetic individual crew travel correction service Approved 0.5 h

2026-10-15 Regular time

BBS DEMO - Técnico 2 BBS ROLE GUIDE - Workshop clean correction vehicle hardware period Approved 2.5 h

2026-10-15 Travel

BBS DEMO - Técnico 2 BBS ROLE GUIDE - synthetic individual crew travel correction service Approved 0.8 h

Technical / PLC records

No technical records in this period.

Client Representative Signature

Name & Title

Date

Please prepare the reviewed period PDF after approving the source records. Use Daily or Technical / PLC to submit your own work; customer sign-off confirms the reviewed period.

Developed by Ricardo Schwendler Souza

Customer-safe operational snapshot prepared by Finance for PM review.

Project Manager · BBS operational course

31 / 79

PM-approved exact customer report version, now Ready for signature.

Review the ready customer version and acceptance queue

Online Go to section ⌘/ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

Dashboard / Daily and technical reports

Print report Search projects, people, invoices... Search

Archived projects are hidden. Include archived projects

Period review and customer follow-up

OPERATIONS / REPORTS Reports 9

Capture field activity, technical changes and customer confirmation in one register.

Project review workflow
Review the operational facts for assigned projects and return incomplete records for correction.
Customer reports contain approved work details without money. Other workers' compensation stays restricted; your own compensation is available separately in My Pay.

New daily report New technical report

Needs attention
0
Draft, submitted, or returned field reports

Ready for signature
1
Customer confirmations awaiting signature

Customer sign-off
1
Period confirmations in scope

Filter reports

Client From
All clients 10/13/2026

To Sort by
10/19/2026 Newest first

Search register Project Status
Project, worker or report C-0050-P-20261005 — BBS - I All statuses

Apply filters Period Today This week This month Last month

Active filters: 3 1 matching records Clear filters

Project: BBS - Ejemplo de manual - C-0050-P-20261005 x From: 2026-10-13 x To: 2026-10-19 x

Daily Technical / PLC Client Sign-off

CUSTOMER CONFIRMATION
Client Sign-off
Confirm approved hours and activities for the selected period.
Open a ready record to review its exact version and record client sign-off. A signed record remains bound to that immutable report version; a source change requires a replacement report.
Workers submit Daily or Technical reports, the Project Manager or Owner reviews the operational facts, Finance or Owner generates the customer-safe period file, and an authorized Owner or Finance user records the customer signed copy.

1-1 / 1

CLIENT SIGN-OFF
BBS - Ejemplo de manual - C-0050-P-20261005
2026-10-13 → 2026-10-19
Ready for signature
Open sign-off record →

Developed by Álvaro Schwiedop Souto

Actual October 13–19 acceptance queue; ready is distinct from signed.

Publish a future plan without creating actual time

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Planning → Publish field assignment

Planning is an expectation and coordination tool. It does not create recorded work or approvals. Planning and worker agendas explicitly display UTC.

The positive BBS exercise published a future October 16 08:00–10:00 UTC assignment for Worker 2, planned 2 hours, fictional bench site and required expertise.

Do the task

1. Open Planning and select BBS in Publish field assignment.
2. Select the existing assigned worker(s). Verify availability and assignment coverage for the intended date.
3. Enter Start (UTC), optional End (UTC), optional Planned hours, Site and Required expertise. Use the actual agreed schedule; do not convert site-local time silently.
4. Choose Publish assignment. Open the October 16 day and the Published schedule record.
5. Confirm the selected worker, UTC start/end and 120 planned minutes. Ask the worker to verify their agenda; they still record actual work independently afterward.

Verify the result

- Native PM Publish assignment succeeded. Worker 2's separate role session saw the published plan.
- A read-only database check found zero BBS actual time entries on October 16 after publication and update.

If you get stuck

- If the worker is absent, verify dated project assignment and availability with Owner/Team. Publishing is not a substitute for project membership.
- If dates are wrong, use the published record's update workflow rather than creating an overlapping duplicate plan.

Publish a future plan without creating actual time

Online

Go to section ⌘/Ctrl K

Webmail

EN

BR BBS ROLE LAB Project Manager Manager

worker records the work performed separately.

Project

C-0050-P-20261005 — BBS · Ejemplo de manual

Workers

Select one or more assigned workers. Each worker receives the same assignment.

☐ BBS DEMO - Jefe de crew

☐ BBS DEMO - Tecnico 1

☒ BBS DEMO - Tecnico 2

☐ BBS ROLE LAB External Technician

☐ BBS ROLE LAB Project Manager

☐ BBS ROLE LAB Supplier Coordinator

Enter dates and times in UTC. The worker agenda also shows times in UTC.

Start (UTC)

10/16/2026, 08:00 AM

End (UTC, optional)

10/16/2026, 10:00 AM

Planned hours (optional)

2.00

Site (optional)

Required expertise

Publish assignment

Actual PM publish form before saving the synthetic future assignment.

Publish a future plan without creating actual time

The screenshot displays the BBS Role Lab Project Manager interface. On the left is a sidebar with navigation options: Dashboard, Projects, Approvals, Reports, SECONDARY, Time, Expenses, My Pay, Team, Planning (highlighted), Documents, Profile, Company Webmail, and Sign out. The main content area shows a form for publishing a field assignment. At the top, there's a header with 'Online', 'Go to section', a search bar, a notification bell, 'Webmail', 'EN', and the user 'BBS ROLE LAB Project Manager'. The form has two columns. The left column contains: 'BBS DEMO - Tecnico 2' (dropdown), 'End (optional)' with '10/16/2026, 10:00 AM' (calendar icon), and 'Site (optional)' (empty text box). The right column contains: '10/16/2026, 08:00 AM' (calendar icon), 'Planned minutes (optional)' with '120' (text box), and 'Required expertise' (empty text box). Below these are 'Save assignment' and 'Cancel assignment' buttons. A section titled 'Publish field assignment' follows, with a note: 'Publish a planned assignment for one or more assigned workers. Planning does not create actual time entries; each worker records the work performed separately.' It includes a 'Project' dropdown set to 'C-0050-P-20261005 — BBS · Ejemplo de manual'. Under 'Workers', it says 'Select one or more assigned workers. Each worker receives the same assignment.' and lists three workers with checkboxes: 'BBS DEMO - Jefe de crew', 'BBS DEMO - Tecnico 1', and 'BBS DEMO - Tecnico 2'.

Online Go to section %/Ctrl K

Webmail EN BBS ROLE LAB Project Manager Manager

BBS DEMO - Tecnico 2 10/16/2026, 08:00 AM

End (optional) 10/16/2026, 10:00 AM

Planned minutes (optional) 120

Site (optional)

Required expertise

Save assignment

Cancel assignment

Publish field assignment

Publish a planned assignment for one or more assigned workers. Planning does not create actual time entries; each worker records the work performed separately.

Project C-0050-P-20261005 — BBS · Ejemplo de manual

Workers Select one or more assigned workers. Each worker receives the same assignment.

☐ BBS DEMO - Jefe de crew

☐ BBS DEMO - Tecnico 1

☐ BBS DEMO - Tecnico 2

Actual PM published plan:120 minutes in UTC, independent of actual work.

Change a published assignment and verify persistence

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Planning → Published schedule → Open record

A published assignment can be edited through its own record. Updating the plan does not correct an actual source that a worker has already submitted.

Do the task

1. Open Published schedule and choose Open record for the correct BBS worker/date.
2. Inspect Worker, Start, End, Planned minutes, Site and Required expertise.
3. Change the intended planning value and choose Save assignment. Reopen the same record to verify the new value.
4. If the assignment should be canceled, use Cancel assignment on that record, then verify its state and tell the affected worker. The separate October 22 cancellation was executed in the historical planning checkpoint; the original positive assignment example remains separate.

Verify the result

- PM changed only the fictional bench site note and Save assignment succeeded; the original worker, date and 2-hour plan remained.
- No October 16 actual time source was created by either publish or update.

If you get stuck

- Check that you opened a planning record, not a time-entry source. Actual submitted work requires the reviewed correction path.
- Coordinate a genuine cancellation with the worker; do not assume a changed plan deletes recorded history.

Change a published assignment and verify persistence

Online Go to section: %/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

C-0050-P-20261005 — BBS · Ejemplo de manual

Workers
Select one or more assigned workers. Each worker receives the same assignment.

- ☐ BBS DEMO - Jefe de crew
- ☐ BBS DEMO - Tecnico 1
- ☐ BBS DEMO - Tecnico 2
- ☐ BBS ROLE LAB Coordinator-recorded Technician
- ☐ BBS ROLE LAB External Technician
- ☐ BBS ROLE LAB Project Manager
- ☐ BBS ROLE LAB Supplier Coordinator

Enter dates and times in UTC. The worker agenda also shows times in UTC.

Start (UTC) mm/dd/yyyy, --:-- --

End (UTC, optional) mm/dd/yyyy, --:-- --

Planned hours (optional) 0

Site (optional)

Required expertise

Publish assignment

Success
Assignment updated.

Sign out

Actual PM Save assignment result after changing the fictional site note.

Follow a shared plan through crew work and review

Isolated BBS planning and crew lab · October 20–25, 2026. Browser-verified synthetic operational records; no real dispatch, payment or customer acceptance. Earlier examples retain their original date scope.

Go here: Planning → October 20; Worker / Chief: Today; Approvals

The Owner published one common October 20 08:00–16:00 UTC plan to the Chief and two existing technicians. This created three planning records, one per person. Their separate Worker-role agendas each showed an eight-hour BBS plan. Project membership and dated chief delegation remained separate prerequisites.

Actual work differed: Technician 1 personally recorded six hours; the Chief recorded seven hours for Technician 2 through the delegated Crew workspace; the Chief personally recorded eight hours. Each source was submitted individually and reviewed by a separate Project Manager account.

Do the task

1. Open Planning, choose October 20 and inspect the three BBS agenda records. Confirm project, worker, UTC interval and 480 planned minutes for each.
2. Ask each worker to check Today → Upcoming assignments using their own account. They do not accept or complete the plan with a task button; they record and report actual work separately.
3. For delegated crew entry, have the Chief check project, date and managed worker before saving individual actual hours. Avoid duplicating a crew-entered source through a worker's own time form.
4. Open Approvals for BBS and October 20. Review the submitted 6 / 7 / 8 hours and operational notes. Choose the supported Approve control for each truthful source.
5. Ask the workers to reopen Time → Week of 2026-10-19. Technician 1 shows Actual 6.00h, Expected 8.00h, Difference –2.00h and Needs note; Technician 2 shows 7.00h / 8.00h / –1.00h and Needs note; Chief shows 8.00h / 8.00h / 0.00h and Approved.

Verify the result

- Native multi-worker publication created no actual time. Later separately authored sources persisted Approved with 360 / 420 / 480 minutes and the correct creator identities.
- Needs note is a weekly comparison indicator for approved time differing from its expectation. The underlying source remains Approved. Explain the work difference in operational notes/reports; never force actual hours to match a target.

Follow a shared plan through crew work and review · continued

If you get stuck

- A chief's ability to record crew time does not automatically grant review authority. Ask the Owner to verify the separate review permission.
- If a worker reports a missing plan, compare today in UTC, project membership and the published plan date. If the actual source is wrong, use the correction chapter rather than editing planning.

Follow a shared plan through crew work and review

Tuesday, October 20, 2026

BBS DEMO - Jefe de crew · C-0050-P-20261005 · 480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 1 · C-0050-P-20261005 · 480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 2 · C-0050-P-20261005 · 480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

Owner-created shared BBS plan visible in the authorized planning agenda: one record per person, each 480 planned minutes.

Follow a shared plan through crew work and review

DAY	ACTUAL	EXPECTED	DIFFERENCE	CATEGORIES	STATUS
Mon 2026-10-19	0.00h	8.00h	-8.00h	—	—
Tue 2026-10-20	6.00h	8.00h	-2.00h	Regular time 6.00h	Needs note
Wed 2026-10-21	0.00h	8.00h	-8.00h	—	—
Thu 2026-10-22	0.00h	8.00h	-8.00h	—	—
Fri 2026-10-23	0.00h	8.00h	-8.00h	—	—
Sat 2026-10-24	0.00h	0.00h	0.00h	—	—
Sun 2026-10-25	0.00h	0.00h	0.00h	—	—
Actual	6.00h	40.00h	-34.00h	Regular time 6.00h	—

Separate Worker 1 view after PM review: six actual hours versus an eight-hour expectation.

Follow a shared plan through crew work and review

October 2026

<
Today
>

Select a day to see its agenda. Times shown in UTC.

Mon	Tue	Wed	Thu	Fri	Sat	Sun
28 .	29 .	30 .	1 .	2 .	3 .	4 .
5 .	6 .	7 .	8 .	9 .	10 .	11 .
12 .	13 .	14 .	15 .	16 1	17 .	18 .
19 .	20 3	21 1	22 1	23 .	24 2	25 1
26 .	27 .	28 .	29 .	30 .	31 .	1 .
2 .	3 .	4 .	5 .	6 .	7 .	8 .

Tuesday, October 20, 2026

BBS DEMO - Jefe de crew · C-0050-P-20261005 · 480 min
Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 1 · C-0050-P-20261005 · 480 min
Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 2 · C-0050-P-20261005 · 480 min
Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

Actual Project Manager calendar at 768-pixel tablet width, with the three October 20 planning records.

Follow a shared plan through crew work and review

Tuesday, October 20, 2026

BBS DEMO - Jefe de crew · C-0050-P-20261005

· 480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 1 · C-0050-P-20261005 ·

480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

BBS DEMO - Tecnico 2 · C-0050-P-20261005 ·

480 min

Oct 20, 2026, 08:00 AM – Oct 20, 2026, 04:00 PM

Actual Project Manager selected-day agenda at 390-pixel phone width. The three worker records display their UTC intervals and planned quantities.

Distinguish planned hours, expected hours and work goals

Isolated BBS planning and crew lab · October 20–25, 2026. Browser-verified synthetic operational records; no real dispatch, payment or customer acceptance. Earlier examples retain their original date scope.

Go here: Planning; Worker: Today and Time; Owner: Projects → Expected Working Schedule

The Owner configures Expected Working Schedule through Projects → More actions. It has an effective date, IANA timezone and a minutes value for each weekday. The BBS lab's October 19 schedule is 480 minutes Monday–Friday and zero on weekends. This reference is separate from published planning and never creates actual work.

The October 21 practice plan was edited to three hours, 09:00–12:00 UTC. Worker 1 sees Planned: 3 h, while the Wednesday timesheet still expects 8.00h and records 0.00h until actual work is entered. Creation displays Planned hours; the edit form displays Planned minutes, so three hours is 180 minutes.

Planning and worker agendas display UTC. On October 20, 08:00–16:00 UTC means 10:00–18:00 Europe/Madrid or 04:00–12:00 America/New_York. Convert for the actual date, because daylight-saving changes can alter the offset.

There is no generic worker-goal Accept / Reject / Mark completed workflow. Use assignments for coordination, expected hours for comparison and Daily / Technical reports for actual progress and blockers. Project milestones are separate project checkpoints; ask the Owner to establish any required milestone configuration.

After the earlier planning tables, the Owner added an explicitly synthetic October 23-only membership for Technician 1 in the existing fictional onboarding project. The later Worker weekly table shows Friday Expected and Difference as — because two own projects cover that day. Earlier screenshots still correctly show Friday eight hours and weekly forty before that extra assignment. No actual work was entered in the second project.

The earlier cancellation screenshots are a historical checkpoint, not the final published-plan count. After later synthetic schedules, the final isolated BBS planning summary contains nine Published assignments and one Cancelled assignment. Cancellation removes that assignment from current published coverage while retaining its history; it creates no actual time.

Do the task

1. Open an existing Published assignments record, edit the interval, Planned minutes and optional site, and choose Save assignment. Reopen it to verify persistence and ask the worker to reload Today.

Distinguish planned hours, expected hours and work goals · continued

2. To cancel a plan, identify the correct project, person and dates and choose Cancel assignment. Check the calendar and the worker's upcoming agenda. Cancellation does not erase or correct an actual-time source.
3. If Today has no plan but lists Your assigned projects, check whether the plan is future or has not been published. Membership alone does not publish a shift.
4. If the worker is unavailable in the publish form, ask the Owner to check active account status and project-assignment coverage for the selected interval. Supplier personnel with coverage ending October 31 are not eligible on November 1.
5. If Expected is —, ask the Owner to check membership and effective schedule dates. Zero is a valid target; — means unknown. Worker 1's September 28–30 precede their October 1 membership and therefore show unknown expectations.
6. If multiple projects cover the day, do not add their targets together yourself. The application leaves the expectation unknown where it lacks a single effective project/schedule. Resolve the planning allocation with the Owner; the later October 23 one-day second-assignment checkpoint demonstrates the unknown target.

Verify the result

- Native PM edit saved 180 minutes, updated UTC dates and site; the Worker agenda reflected those values after reload. The weekly expected eight hours did not change.
- A separate October 22 Worker 2 plan was cancelled natively and disappeared from the Worker agenda. Its retained record has cancelled status and no actual-time source was generated.
- The later separate Worker session showed October 23 Actual 0.00h / Expected — / Difference — while the main October 20 six actual and eight expected hours stayed unchanged. Counting a future own membership for ambiguity did not expose that project in the current selector or add actual records.

If you get stuck

- The External Technician profile has restricted Time / Expenses / Reports access and currently no internal Today agenda or Planning calendar, even when the Owner publishes a plan. Confirm its schedule through the authorized operational handoff.
- Use screenshots and hours comparisons to explain operational issues within your authorized project. Send questions outside that scope to the Owner.
- After a publish-field validation message, correct the highlighted field and recheck the retained person, UTC interval, planned quantity, Site and Required expertise before retrying.

Distinguish planned hours, expected hours and work goals

Published schedule

Published

BBS DEMO - Tecnico 1 · C-0050-P-20261005 · BBS · Ejemplo de manual

Start

2026-10-21 09:00 UTC

End (optional)

2026-10-21 12:00 UTC

Planned minutes (optional)

180 min

Site (optional)

BBS planning lab · updated PM practice bench

Open project →

PM published record reopened after editing: October 21 09:00–12:00 UTC, 180 planned minutes and the saved fictional site.

Project Manager · BBS operational course

47 / 79

Distinguish planned hours, expected hours and work goals

Upcoming assignments

Showing 2 of 2

Published assignments after today, in date order.

Oct 20, 2026 · 08:00 – 16:00 UTC

C-0050-P-20261005

BBS · Ejemplo de manual

BBS planning lab · fictional crew bench

Planned: 8 h

Open project →

Oct 21, 2026 · 09:00 – 12:00 UTC

C-0050-P-20261005

BBS · Ejemplo de manual

BBS planning lab · updated PM practice bench

Planned: 3 h

Open project →

Separate Worker 1 agenda after the edit: the published three-hour practice plan appears alongside the eight-hour crew plan.

Distinguish planned hours, expected hours and work goals

DAY	ACTUAL	EXPECTED	DIFFERENCE	CATEGORIES	STATUS
Mon 2026-10-19	0.00h	8.00h	-8.00h	—	—
Tue 2026-10-20	6.00h	8.00h	-2.00h	Regular time 6.00h	Needs note
Wed 2026-10-21	0.00h	8.00h	-8.00h	—	—
Thu 2026-10-22	0.00h	8.00h	-8.00h	—	—
Fri 2026-10-23	0.00h	8.00h	-8.00h	—	—
Sat 2026-10-24	0.00h	0.00h	0.00h	—	—
Sun 2026-10-25	0.00h	0.00h	0.00h	—	—
Actual	6.00h	40.00h	-34.00h	Regular time 6.00h	—

Separate Worker 1 weekly table: planned three hours does not replace the independently configured eight-hour Wednesday expectation. This is the earlier checkpoint, before the additional October 23 one-day membership; its Friday eight-hour expectation and weekly forty-hour target remain correct for that saved stage.

Distinguish planned hours, expected hours and work goals

BBS DEMO - Tecnico 2 · C-0050-P-20261005 · 2026-10-22 12:00 → 2026-10-22 14:00



Worker

BBS DEMO - Tecnico 2



Start

10/22/2026, 12:00 PM



End (optional)

10/22/2026, 02:00 PM



Planned minutes (optional)

120

Site (optional)

BBS planning lab · cancel practice

Required expertise

Save assignment

Cancel assignment

Actual PM Cancel assignment control for the separate October 22 Worker 2 practice plan. Verify the worker and interval before cancelling.

Distinguish planned hours, expected hours and work goals

Thursday, October 22, 2026

BBS ROLE LAB External Technician · C-0050-P-20261005 · 120 min

Oct 22, 2026, 08:00 AM – Oct 22, 2026, 10:00 AM

October 22 agenda after cancellation: the Worker 2 practice plan has disappeared; the separate external-technician two-hour plan remains.

Distinguish planned hours, expected hours and work goals

DAY	ACTUAL	EXPECTED	DIFFERENCE	CATEGORIES	STATUS
Mon 2026-09-28	0.00h	—	—	—	—
Tue 2026-09-29	0.00h	—	—	—	—
Wed 2026-09-30	0.00h	—	—	—	—
Thu 2026-10-01	0.00h	8.00h	-8.00h	—	—
Fri 2026-10-02	8.00h	8.00h	0.00h	Regular time 8.00h	Approved
Sat 2026-10-03	3.00h	8.00h	-5.00h	Travel 3.00h	Needs note
Sun 2026-10-04	0.00h	0.00h	0.00h	—	—
Actual	11.00h	—	—	Regular time 8.00h · Travel 3.00h	—

Separate Worker 1 historical week: dashes before the October 1 assignment demonstrate an unknown expected target, rather than a zero-hour schedule.

Distinguish planned hours, expected hours and work goals

Published schedule

Published

BBS DEMO - Tecnico 1 · C-0050-P-20261005 · BBS · Ejemplo de manual

Start	End (optional)	Planned minutes (optional)	Site (optional)	Required expertise
2026-10-25 08:00 UTC	2026-10-25 10:00 UTC	120 min	BBS planning lab · preserved PM site	BBS training PLC

Open project →

Additional PM October 25 practice publication reopened after correcting an invalid interval: saved UTC 08:00–10:00, 120 planned minutes, fictional Site and Required expertise. No actual work was generated.

Distinguish planned hours, expected hours and work goals

DAY	ACTUAL	EXPECTED	DIFFERENCE	CATEGORIES	STATUS
Mon 2026-10-19	0.00h	8.00h	-8.00h	—	—
Tue 2026-10-20	6.00h	8.00h	-2.00h	Regular time 6.00h	Needs note
Wed 2026-10-21	0.00h	8.00h	-8.00h	—	—
Thu 2026-10-22	0.00h	8.00h	-8.00h	—	—
Fri 2026-10-23	0.00h	—	—	—	—
Sat 2026-10-24	0.00h	0.00h	0.00h	—	—
Sun 2026-10-25	0.00h	0.00h	0.00h	—	—
Actual	6.00h	—	—	Regular time 6.00h	—

Later isolated checkpoint, after an additional one-day project membership on October 23: Friday Actual is zero and Expected / Difference are unknown (—). October 20 remains six actual versus eight expected hours. Earlier weekly tables precede this added membership and correctly show Friday eight expected hours.

Distinguish planned hours, expected hours and work goals

The screenshot displays the 'Resource planning' interface within the BBS ROLE LAB Project Manager. The interface is divided into several sections:

- Left Sidebar:** Contains navigation links for Dashboard, Projects, Approvals, Reports, Time, Expenses, My Pay, Team, Planning (highlighted), Documents, Profile, and Company Website. A 'Sign out' button is at the bottom.
- Header:** Shows the user's name (J&A / Resource planning), a 'Print report' button, and a search bar for projects, people, and invoices.
- Resource planning section:**
 - October 2026:** A calendar view showing planned hours for each day. The date 'Tuesday, October 6, 2026' is selected.
 - Published assignments:** A list of assignments for the selected date, including roles like 'BBS DEMO - Técnico 2', 'BBS DEMO - Jefe de crew', and 'BBS ROLE LAB External Technician'.
 - Publish field assignment:** A form to create a new assignment, including fields for Project, Workers, Start/End times, Planned hours, and Required expertise.
 - Published schedule:** A table showing the published schedule for the selected project and worker, including dates, times, and status.

Final planning summary after later synthetic schedules: nine Published and one Cancelled; earlier cancellation figures remain historical checkpoints.

Maintain expertise and availability in the correct scope

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Profile → Expertise and availability

Profile lets the PM inspect authorized workforce expertise and availability. Availability windows and Planning use UTC. Account security below the workforce profile concerns your own signed-in account.

The positive exercise saved only the fictional PM's own available October 16 08:00–10:00 UTC window. No other person's real availability was changed.

Do the task

1. Open Profile. Use Inspect worker and View worker profile to confirm whose workforce information is displayed.
2. Choose Add availability. Enter Starts and Ends in UTC, select Available/appropriate status, add the operational note, and choose Save availability.
3. Reopen Profile and inspect the availability window table and calendar day. Check person, dates, times and status.
4. For expertise, use Add expertise, select the appropriate existing skill and proficiency, save, and recheck the table. Skill editing was inspected, not executed in this packet.

Verify the result

- Native PM availability Save succeeded and the reopened table showed the exact fictional October 16 window.
- The separate planning record remained Worker 2's future assignment; availability alone did not publish a plan or create hours.

If you get stuck

- Before changing a workforce record verify the selected person; changing Inspect worker does not switch your authenticated account.
- If the required expertise is absent, ask the Owner to maintain the expertise catalog. Avoid using an unrelated skill as a placeholder.

Maintain expertise and availability in the correct scope

The screenshot displays the 'Profile and security' page in the J&A system. The left sidebar contains navigation links: Dashboard, Projects, Approvals, Reports, SECONDARY (Time, Expenses, My Pay, Team, Planning, Documents), Profile (selected), and Company Webmail. The main content area is titled 'Profile and security' and includes a 'Print report' button and a search bar. The 'WORKFORCE PROFILE' section is active, showing 'Expertise and availability' management. It includes a 'Search team' input, an 'Inspect worker' dropdown menu (currently showing 'BBS ROLE LAB Project Manager · Project manager'), and a 'View worker profile' button. Below this is an 'Add expertise' button. A table section titled 'Scroll horizontally to review all columns.' has columns for 'EXPERTISE', 'PROFICIENCY', and 'VERIFIED', with a note 'No expertise recorded.' Below the table is an 'Availability calendar' section with an 'Add availability' button and a calendar view for 'October 2026' showing 'Today'.

Online Go to section %/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

J&A / Profile and security

Print report Search projects, people, invoices... Search

WORKFORCE PROFILE

Expertise and availability

Review the selected worker's expertise and availability without exposing compensation or client rates.

Search team Inspect worker

BBS ROLE LAB Project Manager · Project manager View worker profile

Add expertise

Scroll horizontally to review all columns.

EXPERTISE	PROFICIENCY	VERIFIED
No expertise recorded.		

Availability calendar

Choose a day to add availability. Open an existing window to edit it. Times are UTC.

Add availability

October 2026

Select a day to see its agenda. Times shown in UTC.

< Today >

Actual PM Profile: saved fictional availability window and own account security.

Record your own operational time and hand it off

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Time → Log time → Save draft → Submit

The PM can record personal operational work separately from reviewing crew facts. The Time register can include authorized people; your source must name the intended worker. My Pay remains personal.

The positive exercise saved 0.50 actual hour on October 8 for the fictional PM's documentation work, then submitted it. It remains pending another authorized reviewer; this packet did not self-approve it.

Do the task

1. Open Time, filter BBS and the intended dates, then choose Log time.
2. Select Assigned project BBS, enter the actual Date, Operational category, Actual hours and Activity summary. Add start/end times only if known.
3. Choose Save draft. Open the saved source and verify the person, date, duration and summary.
4. Choose Submit for the reviewed draft. Confirm Submitted and give its source to another authorized reviewer.
5. For weekly entry, inspect every draft included before Submit all week drafts. Copy previous week layout copies layout; it is not a statement that the work happened. Weekly copy/bulk submission were inspected, not executed in this PM packet.

Verify the result

- The PM source was genuinely saved and Submitted with 30 minutes.
- The source was not approved. Personal My Pay showed a pending estimate rather than proof of payment.

If you get stuck

- Correct an ordinary draft before submission. Once submitted, follow a returned linked correction and explicit resubmission.
- If a source is locked or its correction action is unavailable, send the Owner its ID, project, work date, requested correction and reason.

Record your own operational time and hand it off

WorkerBBS ROLE LAB Project Manager — bbs-role-lab-manager@example.ti **Capture actual work**

Describe what happened on site and record the actual duration.

Assigned projectC-0050-P-20261005 — BBS · Ejemplo de manual **Date**10/08/2026 **Operational category**Work ☐ **Add start and end times****Actual hours**

0.5

Actual duration: 0.5 h

Enter decimal hours, for example 7.5.

Activity summary

SYNTHETIC ROLE LAB: PM own half-hour operational documentation; no live work

**Add a meal expense with these hours**

Cancel

Save draft

Recaptured native form with factual work inputs and the complete Save draft control. Fields are filled for illustration; this capture did not save another source.

Record your own operational time and hand it off

Online Go to section %/Ctrl K

Webmail EN BR BBS ROLE LAB Project Manager Manager

Worker All workers Client All clients

From 10/08/2026 To 10/08/2026

Sort by Newest first Category All categories

Apply filters

Period Today This week This month Last month

Active filters: 3 1 matching records Clear filters

Project: C-0050-P-20261005 — BBS · Ejemplo de manual From: 2026-10-08 To: 2026-10-08

ACTIVITY REGISTER

Recent time entries 1

2026-10-08 · C-0050-P-20261005 Manage record →

Regular time · 0.50h · Submitted

SYNTHETIC ROLE LAB: project manager own operational documentation, no live dispatch.

Open record →

Success Time submitted.

Developed by Álvaro Schwiedop Souto

Actual PM saved-and-submitted half-hour training source.

Inspect receipts and distinguish operational review from repayment

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Expenses → Record expense / Approvals Expenses

Expenses records receipt evidence and operational facts: project, date, category, vendor, currency, amount and who paid. Record the actual purchase facts; reimbursement is a later separate step. The PM operationally approved existing synthetic receipts; PM own expense creation was not executed here.

Do the task

1. Open Expenses and filter BBS, date range, worker, category, currency or Receipt evidence as needed.
2. Open the receipt/source and check the event, amount, currency, payer and any linked logged hours. Required receipt missing needs supporting evidence before submission or review.
3. For your own permitted new expense choose Record expense, enter the factual fields and attach the receipt, then Save draft and inspect it before Submit. This is an inspected reference path in the PM packet.
4. For another submitted expense, go to Approvals → Expenses and Approve correct operational facts or return a specific Required change.
5. Send Finance the approved source for the later reimbursement review and payment process.

Verify the result

- PM operational approvals succeeded for the fictional USD 12 worker supply receipt, USD 20 allocated shared meal and USD 8 external expense.
- No reimbursement date, payee or actual payment was recorded by the PM packet.

If you get stuck

- Never change currency merely to make an amount resemble another view. Check receipt evidence and the actual original spending currency.
- An Approved receipt is not proof of reimbursement; the authorized Finance process and the worker's own payment status provide that check.

Inspect receipts and distinguish operational review from repayment

WORKER OPERATIONS

Expenses

4

Record the amount, currency, payer and receipt for this expense.

Current PM expense workspace: factual purchase entry and operational review.

Read only your own compensation and payment status

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: My Pay → From / Through → Apply period

My Pay identifies your signed-in account's own activity, compensation and reimbursement. Confirm that identity and the selected period before reading the statement.

Estimated compensation, approved compensation, finalized settlement, expected payment date and recorded actual payment mean different things. A settlement is not a bank transfer.

Do the task

1. Open My Pay and select From and Through; choose Apply period.
2. Review approved and pending estimates, Own activity detail, Settlement status and Reimbursement status for that period.
3. Compare the source state with your own estimate. For the PM October 8 half-hour Submitted source, the October 1–31 view showed a pending estimate; it did not prove that payment occurred.
4. For your own statement, confirm From and Through, choose Apply period, then Generate report in Worker statement. If preparing, use Check statement status where offered or refresh after processing. Download PDF and CSV separately only when each is Ready; open each and verify your own identity, selected period and included activity. This sequence is source checked; PM statement generation was not executed in this packet.
5. If an amount or expected payment is wrong, give Finance the source/project/period and the observed difference.

Verify the result

- Native My Pay opened within the signed-in PM's own scope and selected period. A URL query naming a different person did not change that scope.
- The PM packet created no settlement or actual payment.

If you get stuck

- Check period first: the default view ended on the current day, excluding future October 8 training activity.

Read only your own compensation and payment status · continued

- Do not assume an estimate is money owed today or money received. Ask Finance about settlement and payment evidence separately.

Register and retrieve a private project document

Native isolated BBS role exercise · C-0050-P-20261005 · synthetic October 2026 work only

Go here: Documents → Upload document

Sensitivity labels describe content handling. Document audience/access is a separate scope decision. The PM Upload document form exposes Project, Artifact type, Sensitivity, Description and File; it does not expose the Owner's Document access selector.

Register only permitted operational project documents. Ask the Owner to register material needing an audience or access control unavailable in your upload form.

Do the task

1. Select your permitted project, Artifact type, Sensitivity (Internal, Sensitive or Customer private), Description and File. Choose Upload and register hash.
2. Inspect the saved filename, project, sensitivity, byte size, hash and exact scan status. Saved is not the same as scanned clean.
3. Open the native private document link. Compare the retrieved file with the registered content/hash and retain its source identity.

Verify the result

- Native PM document 01a11186-4194-7524-a61a-dcd5a4deb734 was registered within BBS. It is a synthetic operational project note, with no claimed business event. Native private retrieval was executed.

If you get stuck

- If retrieval is denied, verify project scope and document audience with the Owner. Never widen sensitivity or audience to bypass access.

Register and retrieve a private project document

Register a private artifact

Receipts, PLC backups and project reports are validated, hashed and kept outside the public site.

Artifact details

Project Required	Artifact type Required
C-0050-P-20261005 — BBS · Ejemplo de manual	SYNTHETIC TRAINING operational note
Sensitivity	Description Required
Internal	Fictional BBS field notes for the project handover.
File Required	
Choose File No file chosen	

Upload and register hash

Native PM upload form with a fictional operational description. Select the file before Upload and register hash. This capture shows the input stage; it does not register a new document.

Register and retrieve a private project document

The screenshot shows the 'Documents' page in the J&A Project Manager. The sidebar on the left contains navigation links: Dashboard, Projects, Approvals, Reports, SECONDARY (Time, Expenses, My Pay, Team, Planning), Documents (selected), Profile, and Company Webmail. The main content area has a header with 'J&A / Documents', a 'Print report' button, and a search bar. Below the header, there's a section for 'Register a private artifact' and a 'Private project documents' section. The 'Private project documents' section includes a search bar, a 'Sort by' dropdown (set to 'Newest first'), and a list of documents. Each document entry shows the filename, project ID, a brief description, and the file size. To the right of each entry are 'View' and 'Download' buttons, and an 'Archive' dropdown menu. The documents listed are:

- pm06-private-note.txt**: C-0050-P-20261005 - BBS - Ejemplo de manual - All projects. Registered documents are retained as evidence. Upload a corrected file as a new document; the original stays available in the audit history. Files are private, hash-verified, and authorized on every download. 8 files.
- sc05-synthetic-receipt.pdf**: C-0050-P-20261005 - receipt - 1914 bytes.
- sc05-technical-evidence.txt**: C-0050-P-20261005 - report_attachment - 200 bytes.
- synthetic-external-receipt.png**: C-0050-P-20261005 - receipt - 32473 bytes.
- BBS-ROLE-LAB-PM-NOTE.txt**: C-0050-P-20261005 - SYNTHETIC TRAINING note - 187 bytes.
- synthetic-crew-receipt.png**: C-0050-P-20261005 - receipt - 34706 bytes.
- synthetic-training-receipt.png**: C-0050-P-20261005 - receipt - 34818 bytes.
- demo-shared-meal-receipt.png**: C-0050-P-20261005 - receipt - 32535 bytes.

At the bottom of the page, it says 'Developed by Alvaro Schwiedop Souto'.

Saved synthetic private project document and permitted metadata.

Follow a notification to the current permitted source

Native isolated BBS role exercise · C-0050-P-20261005 · synthetic October 2026 work only

Go here: Notifications → source link

A notification is a pointer to an event. It does not approve a source, create a PDF, pay an expense or certify that the source still has the same state. Mark read only changes inbox acknowledgement.

Do the task

1. Open Notifications and read the project/event. Follow the report link rather than assuming the notification text is the current source.
2. In the native exercise Owner approval of PM own Daily 01a11185-3b39-770f-91e5-29cc4809f223 produced a Report approved notification.
3. Follow its link and verify the source is currently Approved. Use a permitted source action: PM generated the own saved report PDF, then refreshed to Ready and downloaded it.

Verify the result

- A populated native notification and its current Approved source were verified. The exercise used Generate report; it did not treat Mark read as a business-state action.

If you get stuck

- If a link is unavailable, verify current project/source scope. Do not borrow an account to follow an old notification.

Follow a notification to the current permitted source

The screenshot displays the J&A Notifications interface. On the left is a sidebar with navigation links: Dashboard, Projects, Approvals, Reports, and a 'SECONDARY' section containing Time, Expenses, My Pay, Team, Planning, Documents, and Profile. At the bottom of the sidebar is a 'Company Webmail' link and a 'Sign out' button. The top header shows 'Online', a 'Go to section' dropdown, a notification bell, 'Webmail', a language dropdown set to 'EN', and the user profile 'BR BBS ROLE LAB Project Manager Manager'. The main content area is titled 'J&A / Notifications' and 'Notifications'. It includes a 'Print report' button and a search bar. Below this is the 'Activity inbox' section, which states 'Review your latest 50 notifications. Filters apply to this list.' and shows '1 Records'. There are filters for 'All 1' and 'Unread 1'. The notification itself is titled 'Report approved' and contains the text: 'SYNTHETIC PM08 own supervisor documentation review; no live site visit - C-0050-P-2026I005 - Oct 6, 2026, 2:02 PM UTC'. It also shows 'Record date: 2026-10-18' and an 'OPEN RECORD' link with a right arrow. At the bottom of the notification card are buttons for 'new', 'Notification details', and 'Mark as read'. The footer of the page reads 'Developed by Álvaro Schwiedop Souto'.

Actual populated Report approved notification.

Follow a notification to the current permitted source

SYNTHETIC PM08 own supervisor documentation review; no live site visit.
C-0050-P-2026005 BBS - Example de manuel 2026-10-06 BBS ROLE LAB Project Manager

PDF
Language: English [Generate report]

Other PDF languages

Document preview
This preview reflects saved data. All authorized source records to change its content.

Actual data

Daily report
C-0050-P-2026005 BBS - Example de manuel 2026-10-06

OPERATIONAL RECORD

Project	C-0050-P-2026005 BBS - Example de manuel	Client	BBS DEMO - Manual
Date	Oct 18, 2026	Manager	BBS ROLE LAB Project Manager
Task	Approved	Task status	No
Site visit	No	Overline indicator	0
Identify reason		Customer contact	

SUMMARY
SYNTHETIC PM08 own supervisor documentation review; no live site visit.

TASKS COMPLETED
Reviewed National Operational document compliances.

PROBLEMS FOUND
-

CORRECTIVE ACTIONS
-

CLIENT DECISIONS
-

OPEN ITEMS
Add next authorized testing exercises.

BLOCKERS
-

NEXT-DAY PLAN
-

DAILY FIELD REPORT

Work date: 2026-10-18 Site visit: No

Shift summary:
SYNTHETIC PM08 own supervisor documentation review; no live site visit.

Tasks completed:
Reviewed National Operational document compliances.

Problems found:
-

Corrective actions:
-

Client decisions:
-

Overline indicator: 0 Field report: -

Blockers:
-

Open items:
Add next authorized testing exercises.

Next-day plan:
-

Customer contact:
No safety flag: -

Create corrected draft

Report attachments
This report is approved for attachments correction. Create an audited correction draft to add new evidence to the correction.
Approved: [Signature]
Report signed correction

Report summary

Project	C-0050-P-2026005 BBS - Example de manuel	Client	BBS DEMO - Manual	Manager	BBS ROLE LAB Project Manager	Task status	No
Task	Approved	Task status	No	Overline indicator	0	Customer contact	

Change history
Viewable only for the report owner.

Daily report approved
Report approved: 2026-10-18 10:00:00
Audit details

Daily report submitted for review
Report submitted for review: 2026-10-18 10:00:00
Review review: 1
Review details: No
Audit details

Daily report created
Report created: 2026-10-18 10:00:00
Audit details

Following the notification reaches the exact currently Approved own report.

Complete own reports and use the shared access/security procedures

Native isolated BBS role exercise · C-0050-P-20261005 · synthetic October 2026 work only

Go here: Own Reports / Expenses / My Pay / Profile / Help

PM own work remains an authored worker source. In the native October 18 exercise PM selected their own Worker, BBS and report date, completed summary/tasks/open items/next-day plan, saved, submitted, and Owner approved the Daily v3.

For invitation and sign-in use Access · activate the invitation and sign in (access). For MFA, devices and recovery use Security · verify your own device and recovery options (security).

For own expenses use Category, Date, Amount, Currency, Who paid, Description, Payment method and private receipt; verify the saved receipt before Submit. Operational approval is distinct from reimbursement. The own-expense procedure is source-checked here, not claimed newly executed.

Use My Pay for your own statement. Check your identity, period, included sources, currency and actual payout state. No new PM payout was created in this exercise.

Do the task

1. For an own report choose yourself in Worker where the form requests it, complete the facts and Save draft. Submit and verify the receiving reviewer and source state.
2. On the approved own Daily select language, Generate report, Refresh until Ready, then Download and compare v3/source identity.
3. Use the shared access/security chapters for actual invitation, MFA, device and recovery procedures. Use Completion check · your permitted role cycle (verification) to distinguish native execution from source-checked references.

Verify the result

- PM own Daily was approved by Owner, generated Ready in English and downloaded natively. This exercised a separate reviewer; it does not assert that every source has a universal self-review denial.

If you get stuck

- For current access or recovery problems follow the shared security recovery instructions and contact the Owner using the approved company channel.

Complete own reports and use the shared access/security procedures

J&A AUTOMATION

×

New daily report

Operational report entry. Record what happened in the field.

Tasks completed

Reviewed fictional handover document completeness.

Problems found

Corrective actions

Downtime minutes

0

Standby reason

Open items

Await next authorized training exercise.

Next-day plan


Safety-related change

Cancel

Save daily report

Actual own PM Daily form; own Worker selected.

Complete own reports and use the shared access/security procedures

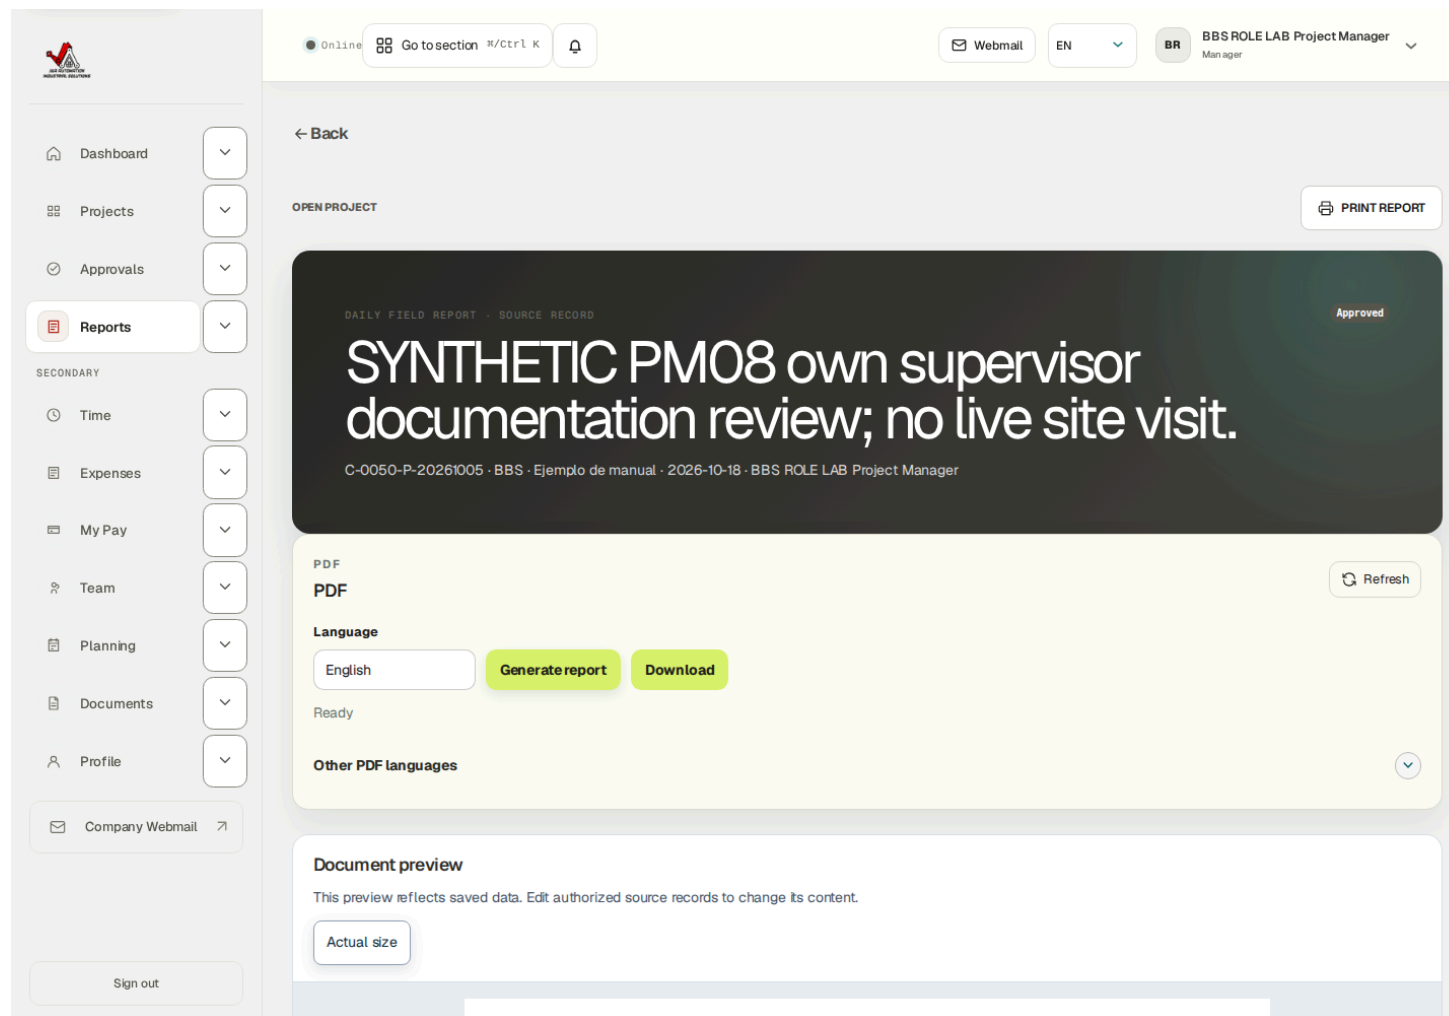

Actual Approved own Daily v3 with Ready English PDF and Download.

Complete the PM operational cycle and hand off

Browser-verified isolated BBS project C-0050-P-20261005. All ROLE LAB records are synthetic training; they are not real dispatch, customer acceptance, purchase or payment.

Go here: Dashboard → Planning → Approvals → Reports

A practical PM day starts with authorized scope and future plans, moves through actual-source review and correction, and ends with report and reimbursement handoffs. Finance handles the reimbursement/payment lifecycle; Owner maintains company access and policy.

Native coverage includes saved/restored membership dates, Reject and Needs changes decisions, author linked recovery and PM approval, actual Approved Technical attribution, Finance-created customer v2 followed by PM approval and Ready signature queue, private document registration and matching retrieval, populated notification to current source, own Daily approval by Owner and Ready PDF download. New Assign worker, own expense and statement generation remain source-checked references. See Completion check · your permitted role cycle (verification).

Do the task

1. Confirm BBS project identity, timezone and your active membership. Check future Planning against availability.
2. Review submitted sources in the correct Approvals tab. Return incorrect facts with precise reasons and re-review submitted linked corrections.
3. Check approved Daily/Technical narratives and the exact customer period queue. Send Finance/Owner the approved source/period handoff.
4. Record personal work under your own source and send it to another reviewer. Check your own My Pay separately.
5. Retain authorized project evidence, investigate processing/access errors, and report unresolved issues with exact source references.

Verify the result

- No live email, customer signature, dispatch, purchase, bank payment or production business mutation occurred in this training packet.
- Earlier BBS records remained unchanged.

Complete the PM operational cycle and hand off · continued

If you get stuck

- Do not solve a locked history problem by duplicating a project or time source. Use the supported correction or Owner handoff.
- When a task belongs to another role, send a clear handoff: source, project, period, state, required result and reason.

Recovery · correct a source or request help

Use your role's worked correction lesson and the controls offered on the current record. Preserve the original. A new purchase is different from correcting an existing purchase.

State	Supported next action
Ordinary Draft	Use Edit/Save draft where present; attach the actual receipt/evidence before Submit. Inspect each saved draft after weekly table entry.
Submitted	Read current state and reviewer handoff. Do not create another source merely because review is pending.
Needs changes	Read the reason. Time uses Create corrected draft where available, then submit/review the linked replacement. A returned Daily/Technical report instead offers Edit and Save changes on the same report, then Submit for review; follow the exact role lesson.
Rejected	Inspect the reason and contact reviewer/Owner. The time detail does not offer the same linked-correction route as Needs changes; do not assume that route exists.
Approved, correction available	Use the offered linked correction and review every value before creating it. Submit the replacement for the authorized reviewer and verify its resulting state.
Locked or correction unavailable	Send the source ID, project, work date, visible state, requested correction and reason to the designated administrator. Do not create a duplicate. Wait for instructions before changing the record.

If you get stuck

- If an action is unavailable to your account, return to your workspace and contact the designated administrator with the record reference and requested action. Do not change dates or people to work around a restriction.

Security · verify your own device and recovery options

Go here: [Profile](#) → [Account security](#); [Profile](#) → [Add availability](#)

Do the task

1. Check Account security identifies YOUR account even when an authorized workforce profile inspection shows another worker above it. Enroll only your own device. MFA is optional in this release.
2. For a passkey, enter Device name and choose Register passkey on the approved secure portal. Complete your device's creation confirmation. Verify Passkey registered for this account, the registered count and named device row. Cancelled/failed registration is not enrollment.
3. To retire your own lost/obsolete passkey, first confirm you retain another working sign-in method. Select Revoke on the exact device and verify Passkey revoked and removal of its row. If you cannot sign in, use the verified support route rather than another person's session.
4. For an authenticator, choose Enable MFA. Keep the setup URI and one-time recovery codes private in the approved password manager. Add the URI to your authenticator, enter its current six-digit Authenticator code and choose Verify MFA. Verify Enabled and Disable MFA appear; enabling without verification is not completed enrollment.
5. At a later MFA sign-in use Six-digit code → Verify and continue. If the authenticator is unavailable, choose Use a recovery code and enter one unused stored code. If neither method is available, contact admin@j-aautomation.com for identity-verified recovery. Do not send recovery codes or the setup URI to support.
6. To remove optional MFA while signed in, choose Disable MFA and verify Not enabled/Enable MFA. Confirm the intended own account before doing so. A successful settings change is separate from recovering a lost account.
7. Where Add availability is offered, fill Starts, Ends, Availability and Note using the displayed time basis, then Save availability. Verify the saved interval/status/note in the list; use Edit availability on that row and save the changed values. Availability is not project membership, a published shift or actual hours.

Security · verify your own device and recovery options

ACCOUNT MFA

Enabled

Authenticator app

MFA is optional. Enabling it returns the setup URI and one-time recovery codes; store them in an approved password manager.

Disabling MFA removes the authenticator check from future sign-ins. Review your account security before continuing.

Disable MFA

Isolated recipient's authenticator setup was verified; the native Enabled state is shown after secret URI/recovery codes disappeared. No usable security material is published.

Completion check · your permitted role cycle

Use the worked lessons for your own role. Historical examples retain their stated dates and states. A procedure labelled reference was checked against the controls; its outcome was not necessarily executed in the illustrated session.

Verify the result

- Confirm your identity, project and dates. Verify the saved and submitted source, its review state, supported correction or administrator handoff and each permitted Ready output. Submission, review and download are separate checkpoints.
